



Agreement No. CE 63/2016 (EP) Environmental Monitoring and Audit for Disposal Facility to the East of Sha Chau (2017-2020) – Investigation

Monthly EM&A Report for Contaminated Mud Pits to the East of Sha Chau and the South of The Brothers – July 2017

Revision 0

11 August 2017

Environmental Resources Management 16/F Berkshire House 25 Westlands Road Quarry Bay, Hong Kong Telephone (852) 2271 3000 Facsimile (852) 2723 5660



www.erm.com





Dredging, Management and Capping of Contaminated Sediment Disposal Facility at Sha Chau and to the South of The Brothers

Environmental Certification Sheet EP-312/2008/A & EP-427/2011/A

Reference Document/Plan

Document/ Plan- to be- Certified / Verified:	Monthly EM&A Report for Contaminated Mud Pits to the East of Sha Chau and the South of The Brothers – July 2017
Date of Report:	11 August 2017
Date prepared by ET:	11 August 2017
Date received by IA:	11 August 2017

Reference EP Condition

Environmental Permit Condition:

Condition 3.4 of EP-312/2008/A and Condition 4.4 of EP-427/2011/A:

4 hard copies and 1 electronic copy of monthly EM&A Report shall be submitted to the Director within 2 weeks after the end of the reporting month. The EM&A Reports shall include a summary of all noncompliance (exceedances) of the environmental quality performance limits (Action and Limit Levels). The submissions shall be certified by the ET Leader and verified by the Independent Auditor. Additional copies of the submission shall be provided to the Director upon request by the Director.

ET Certification

I hereby certify that the above referenced document/plan complies with the above referenced condition of EP-312/2008/A and EP-427/2011/A

he

Jovy Tam, Environmental Team Leader: Date:

11/8/2017

IA Verification

I hereby verify that the above referenced document/plan complies with the above referenced condition of EP-312/2008/A and EP-427/2011/A

Dr Wang Wen Xiong, Independent Auditor:

Vag V Date:

11/8/2017

Agreement No. CE 63/2016 (EP) Environmental Monitoring and Audit for Disposal Facility to the East of Sha Chau (2017-2020) – Investigation

Monthly EM&A Report for Contaminated Mud Pits to the East of Sha Chau and the South of The Brothers – July 2017

Revision 0

Document Code: 0400720_Monthly July 2017_v0.doc

Environmental Resources Management

16/F

Berkshire House 25 Westlands Road Quarry Bay Hong Kong Telephone: (852) 2271 3000 Facsimile: (852) 2723 5660 E-mail: post.hk@erm.com http://www.erm.com

Client:		Proje	ect No	D:		
Civil Eng	gineering and Development Department (CEDD)	040	0720	0		
Summary		Date				
Cannary				ust 2017		
		Appr				
		Аррі	oveu	by.		
Environn	ument presents the Monthly EM&A Report for nental Monitoring and Audit for Disposal Facility to the East hau and the South of The Brothers.	1	l	~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~	2.	2
		Crai	ġΑ.	Reid		
		Part	-			
v0	Monthly EM&A Report for ESC CMPs and SB CMPs	R	c	JT	CAR	11/8/17
Revision	Description	B	y	Checked	Approved	Date
'ERM Hong- Contract with taking accou	has been prepared by Environmental Resources Management the trading name of Kong, Limited', with all reasonable skill, care and diligence within the terms of the h the client, incorporating our General Terms and Conditions of Business and int of the resources devoted to it by agreement with the client.	Distr	ibutic Inte	on ernal		18001:2007 No. OHS 515956
We disclaim scope of the	any responsibility to the client and others in respect of any matters outside the above.	\boxtimes	Pub	olic		BSI
third parties	s confidential to the client and we accept no responsibility of whatsoever nature to to whom this report, or any part thereof, is made known. Any such party relies on their own risk.		Cor	nfidential		001 : 2008 2 No. FS 32515



CONTENTS

1.1	BACKGROUND	1
1.2	Reporting Period	2
1.3	DETAILS OF SAMPLING AND LABORATORY TESTING ACTIVITIES	2
1.4	DETAILS OF OUTSTANDING SAMPLING AND/OR ANALYSIS	3
1.5	BRIEF DISCUSSION OF THE MONITORING RESULTS FOR ESC CMPS	3
1.6	ACTIVITIES SCHEDULED FOR THE NEXT MONTH	9
1.7	STUDY PROGRAMME	10

ANNEXES

ANNEX A	SAMPLING SCHEDULE
ANNEX B	WATER QUALITY MONITORING RESULTS
ANNEX C	DREDGING RECORD FOR ESC CMP VB
ANNEX D	GRAPHICAL PRESENTATIONS
ANNEX E	Study Programme

Agreement No. CE 63/2016 (EP) Environmental Monitoring and Audit for Disposal Facility to the East of Sha Chau (2017-2020) - Investigation

MONTHLY EM&A REPORT FOR JULY 2017

1.1 BACKGROUND

- 1.1.1 The Civil Engineering and Development Department (CEDD) is managing a number of marine disposal facilities in Hong Kong waters, including the Contaminated Mud Pits (CMPs) to the South of The Brothers (SB) and to the East of Sha Chau (ESC) for the disposal of contaminated sediment, and opensea disposal grounds located to the South of Cheung Chau (SCC), East of Tung Lung Chau (ETLC) and East of Ninepins (ENP) for the disposal of uncontaminated sediment. Two Environmental Permits (EPs), EP-312/2008/A and EP-427/2011/A, were issued by the Environmental Protection Department (EPD) to the CEDD, the Permit Holder, on 28 November 2008 and 23 December 2011 for the Dredging, Management and Capping of Contaminated Sediment Disposal Facilities at ESC CMP V and SB CMPs, respectively.
- 1.1.2 Under the requirements of the two EPs for ESC CMP V and SB CMPs, EM&A programmes which encompass water and sediment chemistry, fisheries assessment, tissue and whole body analysis, sediment toxicity and benthic recolonisation studies as set out in the EM&A Manuals are required to be implemented. EM&A programmes have been continuously carried out during the operation of the CMPs at ESC and SB. A review of the collection and analysis of such environmental data from the monitoring programme demonstrated that there had not been any adverse environmental impacts resulting from disposal activities ⁽¹⁾⁽²⁾⁽³⁾⁽⁴⁾⁽⁵⁾. The current programme will assess the impacts resulting from dredging, disposal and capping operations of CMP V as well as capping operations of SB CMPs.

- ERM (2013) Environmental Monitoring and Audit for Contaminated Mud Pit V at East of Sha Chau. Final Report. For CEDD.
- (2) ERM (2014) Environmental Monitoring and Audit for Contaminated Mud Pit V at East of Sha Chau (2012 2017). Final First Annual Review Report. For CEDD.
- (3) ERM (2015) Environmental Monitoring and Audit for Contaminated Mud Pit V at East of Sha Chau (2012 2017). Final Second Annual Review Report. For CEDD.
- (4) ERM (2016) Environmental Monitoring and Audit for Contaminated Mud Pit V at East of Sha Chau (2012 2017). Final Third Annual Review Report. For CEDD.
- (5) ERM (2017) Environmental Monitoring and Audit for Contaminated Mud Pit V at East of Sha Chau (2012 2017). Final Fourth Annual Review Report. For CEDD.

- 1.1.3 The present EM&A programme under *Agreement No. CE 63/2016 (EP)* covers the dredging, disposal and capping operations of the ESC CMP V as well as the capping operations of the SB CMPs (see *Annex A* for the EM&A programme). Detailed works schedule for ESC CMP V and SB CMPs is shown in *Figure 1.1*. In July 2017, the following works were being undertaken:
 - Dredging operation at ESC CMP Vb;
 - Disposal of contaminated mud at ESC CMP Vd; and
 - Capping operation at SB CMP 2.

Figure 1.1 Works Schedule for ESC CMP V and SB CMPs

Pit	Oneration					20)17	7			-						:	20	18	_			_				-			2	019)	Ĩ								_	20)2()		_				20)21	Ī
PIL	Operation	Α	М	J	J	1	A	s	0	Ν	D	J	F	N	Λ	A N	N	J	J	Α	s	0	Ν	D	J	F	М	I A	N	IJ	J	A	۱s	i C	N	D	J	F	М	Α	М	J	J	Α	S	0	N	ID) J	J	F	N
	Dredging																																										Ι									
ESC CMP V	Disposal																																																			
	Capping																																																			
	Dredging																																																			
SB CMP 2	Disposal																																																			
	Capping																																																			

1.2 **REPORTING PERIOD**

1.2.1 This *Monthly EM&A Report for July 2017* covers the EM&A activities for the reporting month of July 2017.

1.3 DETAILS OF SAMPLING AND LABORATORY TESTING ACTIVITIES

- 1.3.1The following monitoring activities were undertaken for ESC CMP V in July
2017:
 - Demersal Trawling for ESC CMPs was undertaken on 5 and 6 July 2017;
 - *Pit Specific Sediment Chemistry of ESC CMP Vd* was undertaken on 12 July 2017;
 - *Routine Water Quality Monitoring of ESC CMP V* was undertaken on 13 July 2017;
 - Water Column Profiling of ESC CMP Vd was undertaken on 14 July 2017;
 - *Sediment Chemistry after a Major Storm of ESC CMPs* was undertaken on 25 July 2017; and
 - *Water Quality Monitoring during Dredging of ESC CMP Vb* was undertaken on 31 July 2017.

1.3.2 No monitoring activities were scheduled to be undertaken for SB CMPs in July 2017.

1.4 DETAILS OF OUTSTANDING SAMPLING AND/OR ANALYSIS


- 1.4.1 No outstanding sampling remained for July 2017.
- 1.4.2 The following laboratory analyses are in progress during the preparation of this monthly report and will be presented in the next monthly report once the data are available:
 - Laboratory analyses of sediment samples collected for *Sediment Chemistry after a Major Storm of ESC CMPs* in July 2017;
- 1.4.3 The following analyses are in progress and will be presented in the corresponding quarterly report:
 - Species identification of the biota samples collected from *Demersal Trawling for ESC CMPs* in July 2017.

1.5 BRIEF DISCUSSION OF THE MONITORING RESULTS FOR ESC CMPS

- 1.5.1Brief discussion of the monitoring results of the following activities for ESC
CMPs is presented in this *Monthly EM&A Report for July* 2017:
 - *Water Quality Monitoring During Dredging of ESC CMP Vb* in July 2017;
 - Water Column Profiling of ESC CMP Vd in July 2017;
 - *Routine Water Quality Monitoring of ESC CMP V in July 2017;*
 - *Pit Specific Sediment Chemistry of ESC CMP Vd* in June and July 2017;
 - Cumulative Impact Sediment Chemistry of ESC CMPs in June 2017; and
 - Sediment Chemistry after a Major Storm of ESC CMPs in June 2017.

- 1.5.2Impact Water Quality Monitoring during Dredging Operations of ESC CMP
Vb July 2017
- 1.5.3 Dredging activities for ESC CMP Vb commenced on 29 July 2017 and water quality monitoring was conducted three times per week during the reporting period starting from 31 July 2017. During each survey day, monitoring was conducted during both mid-ebb and mid-flood tides at two Reference (Upstream) stations and five Impact (Downstream) stations around the dredging operations at ESC CMP Vb. Monitoring was also conducted at one Sensitive Receiver station situated in Ma Wan. A total of eight (8) stations were monitored and locations of the sampling stations are shown in *Figure 1.2*. Levels of Dissolved Oxygen (DO), Turbidity and Suspended Solid (SS) were assessed for compliance with the Action and Limit Levels (see *Table B1* of *Annex B* for details) set in the *Baseline Monitoring Report* ⁽¹⁾.
- 1.5.4 Monitoring results are presented in *Table B2* of *Annex B*. Daily dredging volume in July 2017 is reported in *Annex C*. Levels of DO, Turbidity and SS complied with the Action and Limit Levels at all stations.
- 1.5.5 The results indicated that the dredging operations at ESC CMP Vb did not appear to cause any unacceptable deterioration in water quality during this reporting period. Therefore, no further action, except for those recommended in the Environmental Permit (*EP-312/2008/A*), are considered necessary for the dredging operations.

ERM - Hong Kong, Ltd (2009) Baseline Monitoring Report. For the Civil Engineering & Development Department, Hong Kong SAR Government.

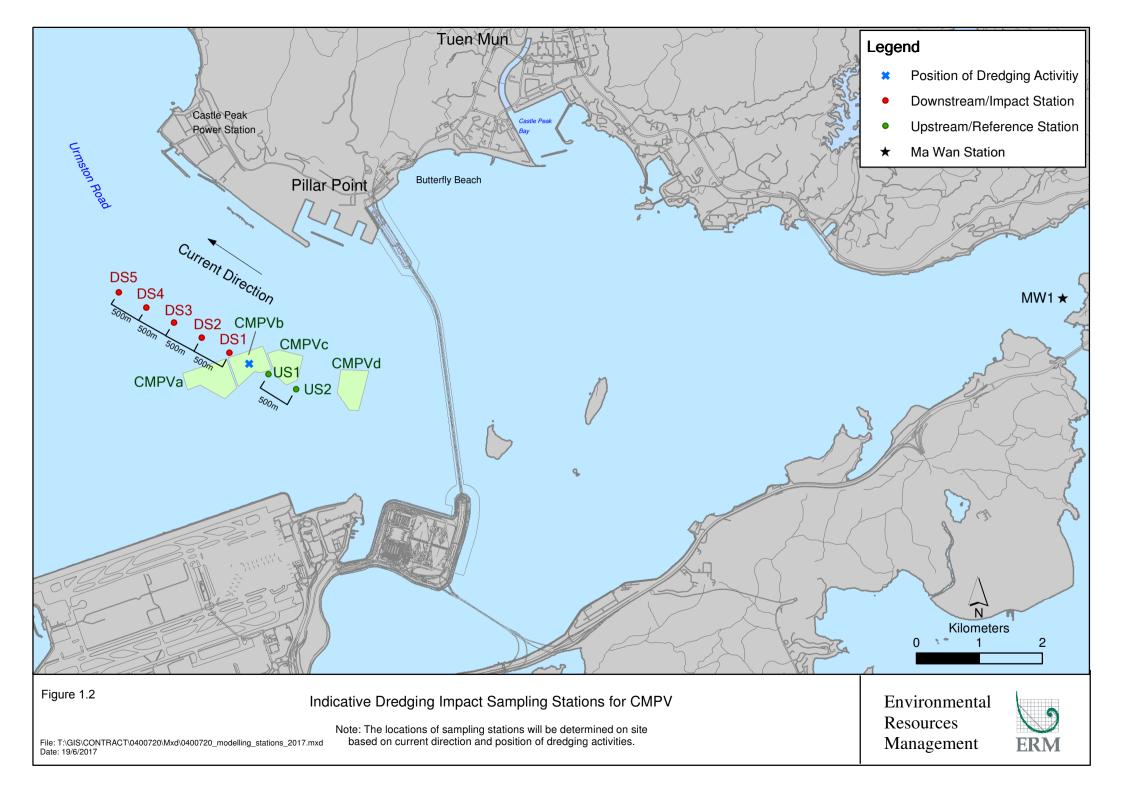

1.5.6 Water Column Profiling of ESC CMP Vd – July 2017

1.5.7 *Water Column Profiling* was undertaken at a total of two sampling stations (Upstream and Downstream stations) on 14 July 2017. The monitoring results have been assessed for compliance with the Water Quality Objectives (WQOs) set by Environmental Protection Department (EPD). This consists of a review of the EPD routine water quality monitoring data for the wet season period (April to October) of 2006 - 2015 from stations in the Northwestern Water Control Zone (WCZ), where the ESC CMPs are located ⁽¹⁾. For Salinity, the averaged value obtained from the Reference (Upstream) station was used for the basis as the WQO. Levels of Dissolved Oxygen (DO) and Turbidity were also assessed for compliance with the Action and Limit Levels (see *Table B1* of *Annex B* for details).

In-situ Measurements

1.5.8 Analyses of results for July 2017 indicated that levels of DO and pH complied with the WQOs at both Downstream and Upstream stations (*Table B3* of *Annex B*). In addition, levels of DO and Turbidity at all stations complied with the Action and Limit Levels (*Tables B1* and *B3* of *Annex B*). Levels of Salinity at Downstream station were higher than the WQO. The higher salinity recorded at Downstream station is likely to be caused by its larger separation distance from the Pearl River mouth, which is a key source of freshwater inputs in the area, when compared to the Upstream station.


Laboratory Measurements for Suspended Solids (SS)

- 1.5.9 Analyses of results for July 2017 indicated that the SS levels complied with the WQO and the Action and Limit Levels at both Upstream and Downstream stations (*Tables B1* and *B3* of *Annex B*).
- 1.5.10 Overall, the monitoring results indicated that the mud disposal operation at ESC CMP Vd did not appear to cause any deterioration in water quality during this reporting period.

⁽¹⁾ http://epic.epd.gov.hk/EPICRIVER/marine/?lang=en


1.5.11	Routine Water Quality Monitoring of ESC CMP V - July 2017
1.5.12	<i>Routine Water Quality Monitoring of ESC CMP V</i> was undertaken on 13 July 2017. The monitoring results have been assessed for compliance with the WQOs (see <i>Section 1.5.3</i> for details). The monitoring results are shown in <i>Tables B4 and B5</i> of <i>Annex B</i> and <i>Figures 1 - 10</i> of <i>Annex D</i> . A total of sixteen (16) monitoring stations were sampled in July 2017 as shown in <i>Figure 1.3</i> .
	In-situ Measurements
1.5.13	Graphical presentation of the monitoring results (Temperature, DO, pH, Salinity and Turbidity) is shown in <i>Figures 1 - 6</i> of <i>Annex D</i> . Analyses of results for July 2017 indicated that the levels of pH, Salinity and DO complied with the WQOs at all stations (Impact, Intermediate, Reference and Ma Wan stations) in July 2017 (<i>Table B4</i> of <i>Annex B; Figures 1, 3</i> and 5 of <i>Annex D</i>).
1.5.14	The levels of DO and Turbidity complied with the Action and Limit Levels at all stations (<i>Table B4</i> of <i>Annex B</i> ; <i>Figures 3</i> and 6 of <i>Annex D</i>).
1.5.15	Overall, <i>in-situ</i> measurement results of the <i>Routine Water Quality Monitoring</i> indicated that the disposal operation at ESC CMP Vd did not appear to cause any unacceptable impacts in water quality in July 2017.
	Laboratory Measurements
1.5.16	Laboratory analysis of July 2017 results indicated that concentrations of Cadmium, Silver and Mercury were below their limit of reporting at all stations. Arsenic, Chromium, Nickel, Lead, Copper and Zinc were detected in July 2017 samples and the concentrations of these metals and metalloids were similar amongst stations (<i>Table B5</i> of <i>Annex B</i> ; <i>Figure 7</i> of <i>Annex D</i>).
1.5.17	For nutrients, concentrations of Total Inorganic Nitrogen (TIN) at all stations in July 2017 were higher than the WQO (0.5 mg/L) (<i>Table B5</i> of <i>Annex B</i> ; <i>Figure</i> <i>8</i> of <i>Annex D</i>). It should be noted that due to the effect of Pearl River, the North Western WCZ has historically experienced higher levels of TIN ⁽¹⁾ . Therefore, the exceedances of TIN WQO at these stations are unlikely to be caused by the disposal operation at ESC CMP Vd. Concentrations of Ammonia Nitrogen (NH ₃ -N) were relatively similar amongst all stations in July 2017 (<i>Table B5</i> of <i>Annex B</i> ; <i>Figure 8</i> of <i>Annex D</i>). Levels of 5-day Biochemical Oxygen Demand (BOD ₅) were higher at Ma Wan station in July 2017 (<i>Table B5</i> of <i>Annex B</i> ; <i>Figure 9</i> of <i>Annex D</i>).
1.5.18	Analyses of results for July 2017 indicated that the SS levels at Impact station were higher than the WQO (11.0 mg/L for wet season), however the concentrations of SS were below the Action and Limit Levels at all stations (<i>Tables B1 and B4</i> of <i>Annex B</i> ; <i>Figure 10</i> of <i>Annex D</i>).


 $(^1) \qquad http://www.epd.gov.hk/epd/misc/marine_quality/1986-2005/textonly/eng/index.htm$

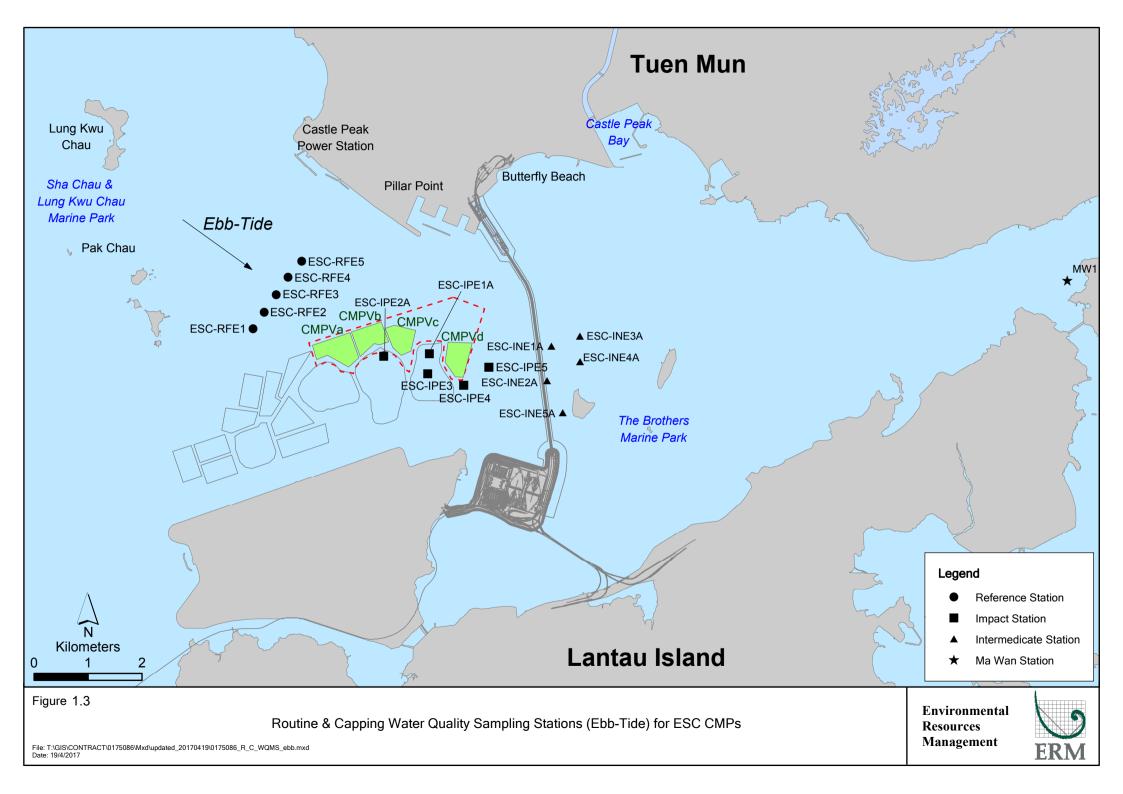

1.5.19 Overall, results of the *Routine Water Quality Monitoring* indicated that the disposal operation at ESC CMP Vd did not appear to cause any unacceptable deterioration in water quality in July 2017. Detailed statistical analysis will be presented in the Quarterly Report to investigate any spatial and temporal trends of potential concern.


- 1.5.20 *Pit Specific Sediment Chemistry of ESC CMP Vd June and July* 2017
- 1.5.21 Monitoring locations for *Pit Specific Sediment Chemistry for ESC CMP Vd* are shown in *Figure 1.4*. A total of six (6) monitoring stations were sampled in June and July 2017.
- 1.5.22 The concentrations of all inorganic contaminants were lower than the Lower Chemical Exceedance Level (LCEL) at all stations in June and July 2017, except Silver, Copper and Zinc in July 2017 (*Figures 11, 12, 15* and *16* of *Annex D*). In July 2017, concentrations of Silver, Copper and Zinc exceeded the LCEL at Active Pit station ESC-NPAA (*Figure 15* of *Annex D*).
- 1.5.23 For organic contaminants, the concentrations of Total Organic Carbon (TOC) were similar amongst the stations in June and July 2017 (*Figures 13* and 17 of *Annex D*). The concentrations of Tributyltin (TBT) were higher at Active Pit stations ESC-NPAA and ESC-NPAB in June and July 2017 (*Figures 14* and *18* of *Annex D*). Low and High Molecular Weight Polycyclic Aromatic Hydrocarbons (PAHs), Total Polychlorinated Biphenyls (PCBs), Total dichloro-diphenyl-trichloroethane (DDT) and 4,4'- dichlorodiphenyldichloroethylene (DDE) concentrations were below the limit of reporting at all stations in June and July 2017.
- 1.5.24 Overall, there is no evidence indicating any unacceptable environmental impacts to sediment quality as a result of the contaminated mud disposal operations at ESC CMP Vd in June and July 2017. Statistical analysis will be undertaken and presented in the corresponding quarterly report to investigate whether there are any unacceptable impacts in the area caused by the contaminated mud disposal.
- 1.5.25 *Cumulative Impact Sediment Chemistry of ESC CMPs June* 2017
- 1.5.26 Monitoring locations for *Cumulative Impact Sediment Chemistry for ESC CMPs* are shown in *Figure 1.5*. A total of nine (9) monitoring stations were sampled in June 2017.
- 1.5.27 Analyses of results for the *Cumulative Impact Sediment Chemistry Monitoring* indicated that the concentrations of all inorganic contaminants were below the LCEL in June 2017 (*Figures 19* and 20 of *Annex D*).
- 1.5.28 For organic contaminants, concentrations of TOC and TBT were recorded to be higher at Ma Wan station (*Figures 21 and 22* of *Annex D*). Low and High Molecular Weight PAHs, PCBs, DDT and DDE concentrations were recorded below the limit of reporting at all stations.
- 1.5.29 Overall, there is no evidence indicating any unacceptable environmental impacts to sediment quality as a result of the contaminated mud disposal operations at ESC CMP Vd in June 2017. Statistical analysis will be undertaken and presented in the corresponding quarterly report to investigate whether there are any unacceptable impacts in the area caused by the contaminated mud disposal.

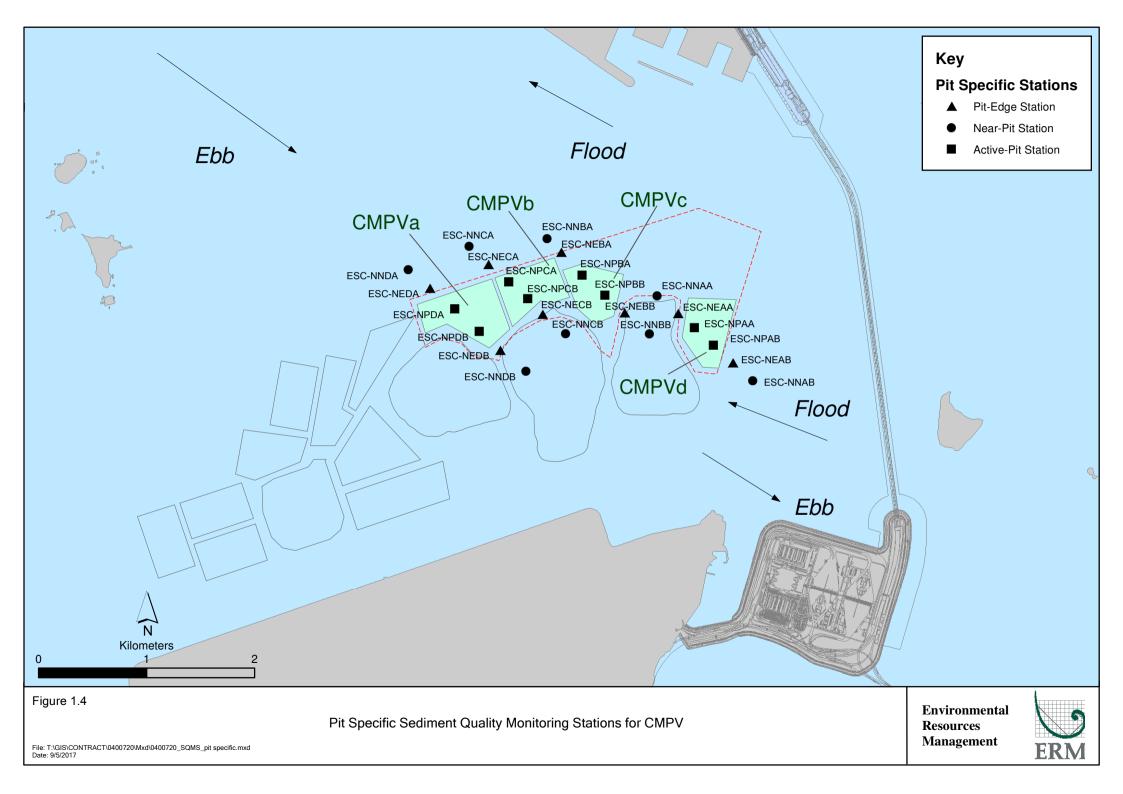

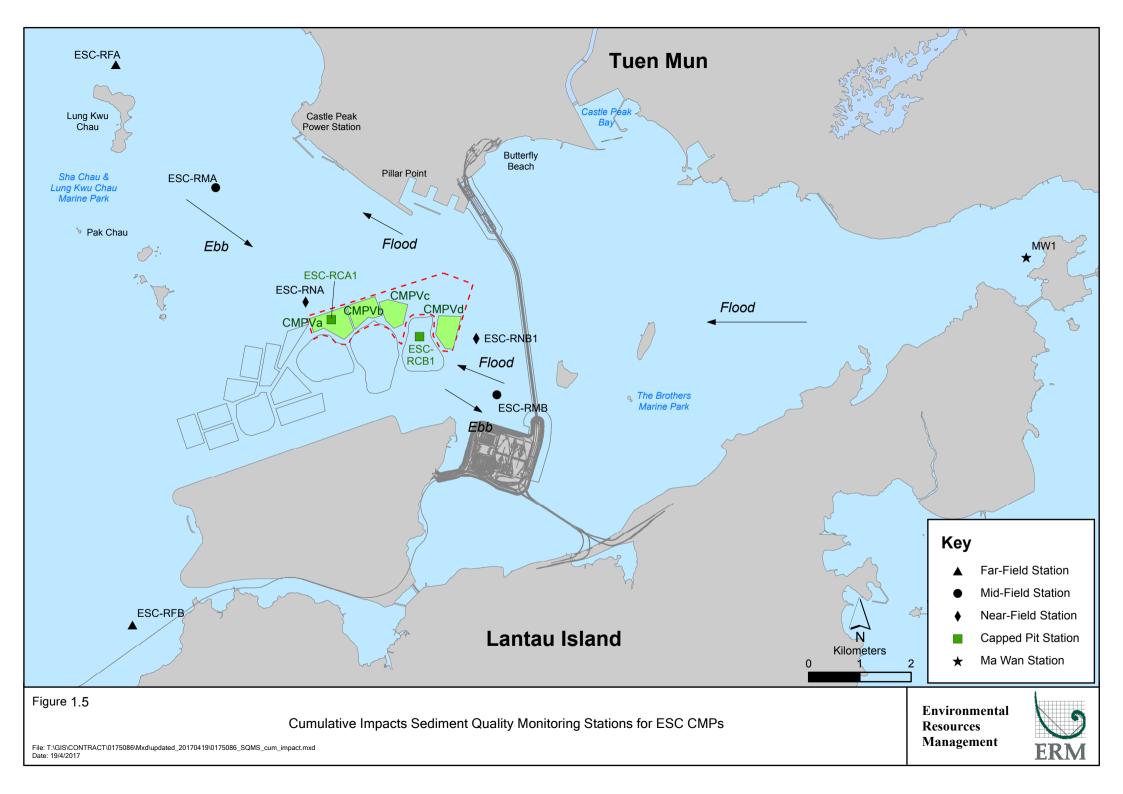

- 1.5.30 Sediment Chemistry after a Major Storm of ESC CMPs June 2017
- 1.5.31 Sampling for Sediment Chemistry after a Major Storm Event was conducted at nine (9) monitoring stations (*Figure 1.5*) on 19 June 2017 after the visit of tropical cyclone Merbok, which led to the issue of Gale or Storm Wind Signal No.8 on 12 June 2017. The track of Merbok is shown in *Figure 1.6*.

Figure 1.6 Track of Tropical Cyclone Merbok from 11 to 13 June 2017 (Source: Hong Kong Observatory)

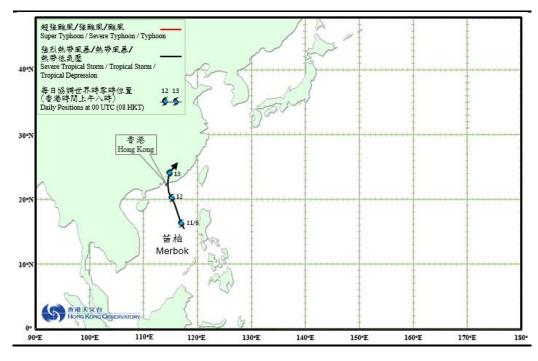

- 1.5.32 Analyses of results for the *Sediment Chemistry after a Major Storm* indicated that the concentrations of all inorganic contaminants were below the LCEL (*Figures* 23 and 24 of *Annex D*).
- 1.5.33 Overall, there appeared to be no evidence showing the failure of CMPs in retaining disposed mud or causing contamination of sediments after the major storm event in June 2017.
- 1.6 ACTIVITIES SCHEDULED FOR THE NEXT MONTH
- 1.6.1 The following monitoring activities will be conducted in the next monthly period of August 2017 for ESC CMP V (see *Annex A* for the sampling schedule):
 - Water Quality Monitoring During Dredging of ESC CMP Vb;
 - Water Column Profiling of ESC CMP Vd;
 - Routine Water Quality Monitoring of ESC CMP Vd;
 - Pit Specific Sediment Chemistry of ESC CMP Vd;

- Cumulative Impact Sediment Chemistry of ESC CMPs;
- Sediment Toxicity Tests of ESC CMPs; and
- Demersal Trawling of ESC CMPs.
- 1.6.2 The following monitoring activities will be conducted in the next monthly period of August 2017 for SB CMPs (see *Annex A* for the sampling schedule):
 - Water Quality Monitoring During Capping of SB CMPs; and
 - Benthic Recolonisation Studies of SB CMPs.

1.7 STUDY PROGRAMME

1.7.1 A summary of the Study programme is presented in *Annex E*.

Annex A

Sampling Schedule

Pit Specific Sediment Chemistry	Code	Frequency	Α		2017 A S	O N	D	J F	M A	2018 M J J	A S	6 O N D	J F	M A	М	2019 J J	A S	O N D	J	F M A		J	A S	0	I D	2021 J F	
Active-Pit	ESC-NPAA ESC-NPAB	Monthly Monthly	12 12	12 12 12 12 12 12	12 12 12 12			12 12 12 12	12 12 12 12		12 12 12 12	2 12 12 12 2 12 12 12 2 12 12 12		12 12 12 12		12 12 12 12	12 12 12 12				12 12 12 12				2 12 1 2 12 1	12 12 12 12	
Pit-Edge	ESC-NEAA ESC-NEAB	Monthly Monthly	12 12	12 12 12 12 12 12					12 12 12 12			2 12 12 12 2 12 12 12						12 12 12 12 12 12								12 12 12 12	
Near-Pit	ESC-NNAA ESC-NNAB		12 12	12 12 12 12 12 12					12 12 12 12			2 12 12 12 2 12 12 12											12 12 12 12			12 12 12 12	
Cumulative Impact Sediment Che Near-field Stations	emistry		A			6 0 N	D	J F				O N D											A S	0 1	I D	J F	М
	ESC-RNA ESC-RNB1	4 times per year 4 times per year		12 12	12 12		12 12	12 12		12 12	12 12	12	12 12			12 12	12 12	12 12		12 12	12		12 12		12 12	12 12	
Mid-field Stations	ESC-RMA ESC-RMB	4 times per year 4 times per year		12 12	12 12		12 12	12 12		12 12	12 12	12 12	12 12			12 12	12 12	12 12		12 12	12		12 12		12 12	12 12	
Capped Pit Stations	ESC-RCA1 ESC-RCB1	4 times per year 4 times per year		12	12 12		12 12	12		12 12	12 12	12	12 12			12 12	12 12	12		12 12	12		12 12		12 12	12	
Far-Field Stations	ESC-RFA ESC-RFB	4 times per year 4 times per year		12	12 12		12 12	12		12 12	12 12	12	12 12			12 12	12 12	12		12	12		12		12 12	12 12	_
Ma Wan Station	MW1	4 times per year 4 times per year		12	12		12	12		12	12	12	12			12	12	12		12	12		12		12	12	
Sediment Toxicity Tests Near-Pit Stations			A	M J J	A S	6 0 N	D	J F	M A	M J J	A S	OND	J F	M A	M	JJ	A S	O N D	J	F M A	M J	J	A S	0 1	I D	J F	М
Reference Stations	ESC-TDA ESC-TDB1	2 times per year 2 times per year			5 5			5			5 5		5				5 5			5			5 5			5 5	
	ESC-TRA ESC-TRB	2 times per year 2 times per year			5 5			5 5			5 5		5				5 5			5			5 5			5 5	
Ma Wan Station	MW1	2 times per year			5			5			5		5				5			5		1 1	5			5	
Tissue/ Whole Body Sampling Near-Pit Stations	ESC-INA	2 times per year	A	M J J	*		D	J F *	MA	MJJ	*	O N D	J F *	MA	м	JJ	A S	O N D	J	F M A	M J	J	A S			J F *	M
Reference North	ESC-INB TNA	2 times per year 2 times per year			*			*			*		*				*			*			*		\mp	*	
Reference South	TNB	2 times per year			*			*			*		*				*			*			*			*	
	TSA TSB	2 times per year 2 times per year			*			*			*		*				*			*			*			*	
Demersal Trawling Near Pit Stations	ESC-INA	4 times per year	A	M J J 5	A S	O N	D	J F 5 5	M A	M J J 5		OND	J F 5 5	M A	M	J J 5	A S	O N D		F M A 5	M J		A S	0 1		J F 5 5	M
Reference North	ESC-INB	4 times per year		5	5			5 5		5	5		5 5		H	5	5		5	5		5	5	Ħ		5 5	
Reference South	TNA TNB	4 times per year 4 times per year		5	5			5 5 5 5		5	5		5 5 5 5			5	5		5 5	5		5	5	╞		5 5 5	
	TSA TSB	4 times per year 4 times per year		5				5 5 5 5		5			5 5 5 5		\square	5 5	5 5		5 5	5 5			5 5			5 5 5 5	
Capping Ebb Tide			A	M J J	A S	O N	D	J F	M A	M J J	A S	OND	J F	M A	M	l l	A S	O N D	J	F M A	M J	J	A S	0 1	I D	J F	M
Impact Station Downcurrent	ESC-IPE1A ESC-IPE2A	4 times per year 4 times per year	H							3	3	3	3		╞	3	3	3	H	3 3	3		3		3	3	
	ESC-IPE3 ESC-IPE4 ESC-IPE5	4 times per year 4 times per year 4 times per year								3 3 3	3 3 3	3 3 3	3 3 3			3 3 3	3 3 3	3 3 3		3 3 3	3		3 3 3		3 3 3	3 3	_
Intermediate Station Downcurrent	ESC-INE1A	4 times per year								3	3	3	3			3 3	3 3	3		3 3	3		3		3	3	
		4 times per year 4 times per year 4 times per year								3	3	3	3			3 3	3 3	3		3 3	3		3 3		3	3	
Reference Station Upcurrent	ESC-INE5A ESC-RFE1	4 times per year 4 times per year								3	3	3	3			3	3	3		3	3		3		3	3	
	ESC-RFE2 ESC-RFE3 ESC-RFE4	4 times per year 4 times per year 4 times per year								3 3 3	3 3 3	3 3 3	3 3 3			3 3 3	3 3 3	3 3 3		3 3 3	3		3 3 3		3 3 3	3 3 3	
Ma Wan Station	ESC-RFE5	4 times per year								3	3	3	3			3	3	3		3	3		3		3	3	
Flood Tide Impact Station Downcurrent	MW1	4 times per year								3	3	3	3			3	3	3		3	3		3		3	3	
	ESC-IPF1 ESC-IPF2 ESC-IPF3	4 times per year 4 times per year 4 times per year								3 3 3	3 3 3	3	3			3 3 3	3 3	3 3 3		3 3 3 3	3		3 3 3		3 3 3	3 3 3	
Intermediate Station Downcurrent	ESC-INF1 ESC-INF2	4 times per year								3	3	3	3			3	3	3		3	3		3 3		3	3	
Reference Station Upcurrent	ESC-INF3	4 times per year 4 times per year								3	3	3	3			3	3	3		3	3		3		3	3	
	ESC-RFF1A ESC-RFF2A ESC-RFF3	4 times per year 4 times per year 4 times per year								3 3 3	3 3 3	3 3 3	3 3 3			3 3 3	3 3 3	3 3 3		3 3 3	3 3 3		3 3 3		3 3 3	3 3 3	
Ma Wan Station	MW1	4 times per year								3	3	3	3			3	3	3		3	3		3		3	3	
Routine Water Quality Monitorin Ebb Tide	g		A	M J J	A S	O N	D	J F	M A	M J J	A S	O N D	J F	M A	М	l l	A S	O N D	J	F M A	M J	J	A S	0 1	1 D	J F	Μ
Impact Station Downcurrent	ESC-IPE1A ESC-IPE2A ESC-IPE3 ESC-IPE4	8 times per year 8 times per year 8 times per year 8 times per year	8 8 8 8	8 8 8 8 8 8 8 8 8 8	8 8 8 8	8 8 8 8 8 8 8 8		8 8 8 8 8 8 8 8	8 8 8 8	8 8 8 8	8	8 8 8 8 8 8 8 8 8 8	8 8 8 8 8 8 8 8			8 8 8 8	8 8 8 8	8 8 8 8 8 8 8 8			8 8 8 8	8 8	8 8 8 8	8 8 8 8 8 8	8	8 8 8 8 8 8 8 8	
Intermediate Station Downcurrent	ESC-IPE5	8 times per year 8 times per year	8	8 8		8 8	F	8 8 8 8	8	8 8	8	8 8	8 8 8 8	8	8	8	8	8 8	8	8 8 8 8	8	8	8	8 8	8	8 8	
	ESC-INE1A ESC-INE2A ESC-INE3A ESC-INE4A	8 times per year 8 times per year 8 times per year 8 times per year	8 8 8	8 8 8 8 8 8 8 8	8 8	8 8 8 8 8 8 8 8		8 8 8 8 8 8 8 8	8 8 8	8 8 8 8		8 8 8 8 8 8 8 8	8 8 8 8 8 8 8 8	8	8 8 8 8	8 8 8 8	8 8 8 8	8 8 8 8 8 8 8 8	8 8 8	8 8 8 8	8 8 8 8	8 8	8	8 8 8 8 8 8	8	8 8 8 8 8 8 8 8	
Reference Station Upcurrent	ESC-INE5A	8 times per year	8	8 8	8	8 8		8 8	8	8 8	8	8 8	8 8	8	8	8	8	8 8	8	8 8	8	8	8	8 8	8	8 8	
	ESC-RFE1 ESC-RFE2 ESC-RFE3	8 times per year 8 times per year 8 times per year	8 8 8	8 8 8 8 8 8	8 8	8 8 8 8 8 8		8 8 8 8 8 8	8 8 8	8 8 8 8	8 8	8 8 8 8 8 8	8 8 8 8 8 8		8 8	8 8 8	8 8 8	8 8 8 8 8 8	8 8		8 8 8	8 8		8 8 8 8 8 8	8	8 8 8 8 8 8	
Ma Wan Station	ESC-RFE4 ESC-RFE5	8 times per year 8 times per year	8 8	8 8 8 8		8 8 8 8		8 8 8 8	8	8 8	8	8 8 8 8	8 8 8 8	8	8	8	8	8 8 8 8	8		8	8	8	88	8	8 8 8 8	
Flood Tide	MW1	8 times per year	8	8 8	8	8 8	Ħ	8 8	8	8 8	8	8 8	8 8	8	8	8	8	8 8	8	8 8	8	8	8	8 8	3	8 8	7
Impact Station Downcurrent	ESC-IPF1 ESC-IPF2	8 times per year 8 times per year	8 8	8 8 8 8	8 8	8 8 8 8			8	8 8 8 8		8 8 8 8	8 8 8 8	8		8	8	8 8 8 8	8 8	8 8 8 8	8 8	8	8	8 8	8	8 8 8 8	
Intermediate Station Downcurrent	ESC-IPF3 ESC-INF1	8 times per year 8 times per year	8	8 8 8 8	8	8 8 8 8			8	8 8 8 8		8 8 8 8	8 8 8 8	8		8	8	8 8 8 8	8	8 8 8 8	8		8	8 8		8 8 8 8	
Reference Station II-	ESC-INF2 ESC-INF3	8 times per year 8 times per year	8	8 8 8 8	8	8 8 8 8			8	8 8	8	8 8 8 8	8 8 8	8	8	8	8	8 8 8 8	8	8 8	8	8			8	8 8 8	
Reference Station Upcurrent	ESC-RFF1A ESC-RFF2A	8 times per year	8 8	8 8 8 8	8	8 8 8 8			8	8 8 8 8	8	8 8 8 8	8 8 8 8	8	8	8	8	8 8 8 8		8 8 8 8	8	8	8	8 8	8	8 8 8 8	
Ma Wan Station	ESC-RFF3 MW1	8 times per year 8 times per year	8	8 8 8 8		8 8 8 8			8			8 8 8 8	8 8 8 8	8	8 8	8	8 8	8 8 8 8	8 8	8 8 8 8	8	8	8 8	88		8 8 8 8	
Water Column Profiling			Α	M J J	A S	6 0 N			M A	M J J	A S	O N D	J F	M A	M			O N D	J	F M A		J		0	N D	J F	
Plume Stations	WCP1 WCP2	Monthly Monthly	4	4 4 4	4 4	4 4	4	4 4	4 4	4 4 4	4 4	$\begin{array}{c ccccccccccccccccccccccccccccccccccc$	4 4	4 4	4	4 4	4 4	4 4 4	4	4 4 4	4 4	4	4 4	4 4	4 4	4 4	4
Benthic Recolonisation Studies Capped Stations at CMPV	ESCV-CPA	2 times per year	A	M J J	A S	O N	D	J F	M A	M J J	A S	OND	J F	M A	M	JJ	A S	O N D	J	F M A	M J	J	A S	0 1	I D	J F	Μ
	ESCV-CPB ESCV-CPC	2 times per year 2 times per year 2 times per year 2 times per year	E		\square						Ħ					+			Ħ		\square	Ħ		Ħ	\ddagger		
Reference Stations	RBA	2 times per year	E								Ħ				\square				Ħ						\pm		
	RBB RBC1	2 times per year 2 times per year	\vdash												\vdash							+		H	$\pm $		
				MII																							

Impact Monitoring for Dredging			Α	Μ	JJ	Α	S	0	N E) J	F	Μ	Α	Μ	J	J.	A S	6 0	Ν	D	J	F	Μ	AN	ИJ	J	Α	S	0	NI	J	F	Μ	A 1	M J	IJ	Α	s	0	NΓ) J	FM	í I
Upstream Stations																																											٦
-	US1	3 times per week			2	2	2																																				
	US2	3 times per week			2	2	2																																				
Downstream Stations																																											
	DS1	3 times per week			2	2	2																																				
	DS2	3 times per week			2	2	2																																				
	DS3	3 times per week			2	2	2																																				
	DS4	3 times per week			2	2	2																																				٦
	DS5	3 times per week			2	2	2																																				٦
Ma Wan Station																																											٦
	MW1	3 times per week			2	2																																					٦

Notes: The number shown in each cell represents the numbers of replicates per monitoring station Impact Monitoring for Dredging will be scheduled when dredging operations commence. Benthic Recolonisation Studies for CMP V will be scheduled when capping operation for CMP V is completed.

Annex A2 - Environmental Monitoring and Audit Sampling Schedule for South of The Brothers (April 2017 - December 2018)

							2017												2018				
Capping Water Quality Monitoring			Α	М	I	I	Α	s	0	Ν	D	I	F	М	А	М	I	I	Α	s	0	Ν	D
Ebb Tide					,	,			-			,								-	-		
Impact Stations Downcurrent																							
1	SB-IPE1	4 times per year		3	3		3				3												
	SB-IPE2	4 times per year		3	3		3				3												
	SB-IPE3	4 times per year		3	3		3				3												
	SB-IPE4	4 times per year		3	3		3				3												
	SB-IPE5	4 times per year		3	3		3				3												
Intermediate Stations Downcurrent																							
	SB-INE1	4 times per year		3	3		3				3												
	SB-INE2	4 times per year		3	3		3				3												
	SB-INE3	4 times per year		3	3		3				3												
	SB-INE4	4 times per year		3	3		3				3												
	SB-INE5	4 times per year		3	3		3				3										<u> </u>		
Reference Stations Upcurrent	CD DEE4			-	_		-				_										<u> </u>		
	SB-RFE1	4 times per year		3	3		3				3										<u> </u>		
	SB-RFE2	4 times per year		3	3		3				3										<u> </u>		
	SB-RFE3	4 times per year		3	3		3				3										<u> </u>		
	SB-RFE4 SB-RFE5	4 times per year		3	3		3				3										<u> </u>		
Constitution Result on Charling	5D-RFE5	4 times per year		3	3		3				3										<u> </u>		
Sensitive Receiver Stations	1 (14/4	4.6		3	3		3				3										i		
	MW1 THB1	4 times per year		3	3		3				3										i		
	THB1 THB2	4 times per year	-	3	3		3				3												
	WSR45C	4 times per year 4 times per year	-	3	3		3				3												
	WSR45C WSR46	4 times per year	-	3	3		3				3												
Flood Tide	115140	4 unics per year		5	5		5				5								-	-	-		
Impact Stations Downcurrent																							
impact stations bowncurrent	SB-IPF1	4 times per year	-	3	3		3				3												
	SB-IPF2	4 times per year	-	3	3		3				3										-		
	SB-IPF3	4 times per year	-	3	3		3				3										-		
Intermediate Stations Downcurrent		i unico per yeur	-	0	Ŭ		Ŭ																
Interintediate Stations Downeartent	SB-INF1	4 times per year	-	3	3		3				3												
	SB-INF2	4 times per year	-	3	3		3				3										-		
	SB-INF3	4 times per year	-	3	3		3				3										-		
Reference Stations Upcurrent				-																			
· · · · · · · · · · · · · · · · · · ·	SB-RFF1	4 times per year		3	3		3				3												
	SB-RFF2	4 times per year		3	3		3				3												
	SB-RFF3	4 times per year		3	3		3				3												
Sensitive Receiver Stations		* *																					
	MW1	4 times per year		3	3		3				3												
	THB1	4 times per year		3	3		3				3												
	THB2	4 times per year		3	3		3				3												
	WSR45C	4 times per year		3	3		3				3												
	WSR46	4 times per year		3	3		3				3												
											_			_			_					_	
Benthic Recolonisation Studies			Α	Μ	J	J	Α	s	0	Ν	D	J	F	Μ	Α	Μ	J	J	Α	S	0	Ν	D
Capped Contaminated Mud Pits			T		1																		
	SB-CPA	2 times per year					12				12								12				12
	SB-CPB	2 times per year					12				12								12				12
Reference Stations			-																				
	RBA	2 times per year					12				12								12				12
	RBA RBB	2 times per year 2 times per year					12 12				12 12 12								12 12				12 12 12

Notes: The number shown in each cell represents the numbers of replicates per monitoring station Capping works are planned to be conducted between May and December 2017.

Annex B

Water Quality Monitoring Results

Parameter	Action Level	Limit Level
Dissolved Oxygen (DO) (1)	Surface and Mid-depth (2)	Surface and Mid-depth ⁽²⁾
	5%-ile of baseline data for surface and	1%-ile of baseline data for surface and
	middle layer = 3.76 mg L -1	middle layer = 3.11 mg L -1 ⁽³⁾
	and	and
	Significantly less than the reference stations mean DO (at the same tide of the same day)	Significantly less than the reference stations mean DO (at the same tide of the same day)
	Bottom 5%-ile of baseline data for bottom layers = 2.96 mg L -1	<u>Bottom</u> The average of the impact station readings are <2 mg/L ⁻¹
	and	and
	Significantly less than the reference stations mean DO (at the same tide of the same day)	Significantly less than the reference stations mean DO (at the same tide of the same day)
Depth-averaged Suspended Solids (SS) ^{(4) (5)}	95%-ile of baseline data for depth average = 37.88 mg L ⁻¹	99%-ile of baseline data for depth average = 61.92 mg L -1
	and	and
	120% of control station's SS at the same tide of the same day	130% of control station's SS at the same tide of the same day
Depth-averaged Turbidity (Tby) ^{(4) (5)}	95%-ile of baseline data = 28.14 NTU	99%-ile of baseline data = 38.32 NTU
	and	and
	120% of control station's Tby at the same tide of the same day	130% of control station's Tby at the same tide of the same day

Table B1Action and Limit Levels of Water Quality for Dredging, Disposal and
Capping Activities at ESC CMP V

Notes:

(1) For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.

(2) The Action and Limit Levels for DO for Surface & Middle layers were calculated from the combined pool of baseline surface layer data and baseline middle layer data.

(3) Given the Action Level for DO for Surface & Middle layers has already been lower than 4 mg L⁻¹, it is proposed to set the Limit Level at 3.11 mg L⁻¹ which is the first percentile of the baseline data.

(4) "Depth-averaged" is calculated by taking the arithmetic means of reading of all three depths.

(5) For turbidity and SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

Sampling	Tidal	Station	Average	DO Levels	Average	Average SS
Date	Period		(n	ng/L)	Turbidity	Level
			Bottom	Surface and	Level	(mg/L)
				Mid Depth	(NTU)	
2017/07/31	Mid-Ebb	DS1	3.83	4.67	7.67	6.75
		DS2	3.73	4.71	6.23	6.10
		DS3	3.97	4.95	5.18	5.35
		DS4	3.34	4.38	5.92	7.28
		DS5	3.93	4.75	5.77	5.72
		US1	3.94	4.83	7.90	4.88
		US2	4.27	4.89	4.53	5.08
		MW1	3.31	5.14	3.16	4.32
	Mid-Flood	DS1	3.90	4.89	7.65	8.43
		DS2	4.24	5.11	7.23	9.42
		DS3	4.26	5.06	6.68	9.63
		DS4	4.30	5.38	6.36	8.47
		DS5	4.29	5.25	6.03	9.33
		US1	4.49	5.21	4.44	8.12
		US2	4.32	5.30	5.15	7.42
		MW1	3.08	4.77	3.47	4.32

Table B2Summary Table of DO, Turbidity and SS Levels Recorded in July 2017 for
Impact Water Quality Monitoring during Dredging Operations of ESC CMP
Vb

Table B3Water Column Profiling Results for ESC CMP Vd in July 2017

Clattere	Temp	Salinity	Turbidity	Dissolved	l Oxygen	pН	Suspended Solids
Stations	(°C)	(ppt)	(NTU)	(%)	(mg L- 1)		(mg L-1)
WCP 1	27.41	19.73	3.91	82.63	5.85	7.91	4.63
(Downstream) WCP 2 (Upstream)	27.94	16.47	4.56	85.38	6.10	7.88	4.78
WQO (Wet season)	N/A	18.19 – 14.88#	N/A	N/A	>4	6.5-8.5	11.0

Note:

*Not exceeding 10% of natural ambient level which is the result obtained from the Reference Station.

Cell shaded yellow / red indicate value exceeding the Action/Limit levels. Cell shaded grey indicate value exceeding the WQO.

Table B4In-situ Monitoring Results for Routine Water Quality Monitoring of ESC
CMPs in July 2017

Sampling Period	Stations	Temp	Salinity	Turbidity	Dissolve	pН	
	Stations	(°C)	(ppt)	(NTU)	(%)	(mg L-1)	(mg L-1)
July 2017	RFE (Reference)	27.08	18.41	6.79	59.04	4.24	7.75
	IPE (Impact)	27.06	18.74	15.74	58.34	4.18	7.75
	INE (Intermediate)	27.06	19.29	6.75	64.39	4.60	7.81
	Ma Wan	27.45	18.94	2.80	89.45	6.36	7.97
	WOO	N/A	16.57 -	N/A	N/A	>4	6.5-8.5
	WQU	1N/A	20.25#	1N/A	1N/A	~4	0.3-8.5

Notes:

*Not exceeding 10% of natural ambient level which is the result obtained from the Reference Station.

Cell shaded yellow / red indicate value exceeding the Action/Limit levels.

Table B5Laboratory Results for Routine Water Quality Monitoring of ESC CMPs in
July 2017

Sampling	Stations	As	Cd	Cr	Cu	Pb	Hg	Ni	Ag	Zn	NH ₃	TIN	BOD ₅	SS
Period	Stations	(µg/L)	(µg/L)	(µg/L)	(µg/L)	(µg/L)	(µg/L)	(µg/L)	(µg/L)	(µg/L)	(mg/L)	(mg/L)	(mg/L)	(mg/L)
July 2017	RFE	2.47	<lor< td=""><td>0.61</td><td>1.38</td><td>0.53</td><td><lor< td=""><td>1.96</td><td><lor< td=""><td>39.68</td><td>0.07</td><td>1.05</td><td>2.13</td><td>7.66</td></lor<></td></lor<></td></lor<>	0.61	1.38	0.53	<lor< td=""><td>1.96</td><td><lor< td=""><td>39.68</td><td>0.07</td><td>1.05</td><td>2.13</td><td>7.66</td></lor<></td></lor<>	1.96	<lor< td=""><td>39.68</td><td>0.07</td><td>1.05</td><td>2.13</td><td>7.66</td></lor<>	39.68	0.07	1.05	2.13	7.66
	IPE	2.83	<lor< td=""><td>0.62</td><td>0.50</td><td>1.07</td><td><lor< td=""><td>2.11</td><td><lor< td=""><td>43.88</td><td>0.05</td><td>0.95</td><td>1.19</td><td>15.72</td></lor<></td></lor<></td></lor<>	0.62	0.50	1.07	<lor< td=""><td>2.11</td><td><lor< td=""><td>43.88</td><td>0.05</td><td>0.95</td><td>1.19</td><td>15.72</td></lor<></td></lor<>	2.11	<lor< td=""><td>43.88</td><td>0.05</td><td>0.95</td><td>1.19</td><td>15.72</td></lor<>	43.88	0.05	0.95	1.19	15.72
	INE	2.68	<lor< td=""><td>0.67</td><td>0.50</td><td>0.50</td><td><lor< td=""><td>2.16</td><td><lor< td=""><td>38.92</td><td>0.06</td><td>0.94</td><td>1.43</td><td>8.59</td></lor<></td></lor<></td></lor<>	0.67	0.50	0.50	<lor< td=""><td>2.16</td><td><lor< td=""><td>38.92</td><td>0.06</td><td>0.94</td><td>1.43</td><td>8.59</td></lor<></td></lor<>	2.16	<lor< td=""><td>38.92</td><td>0.06</td><td>0.94</td><td>1.43</td><td>8.59</td></lor<>	38.92	0.06	0.94	1.43	8.59
	Ma Wan	2.35	<lor< td=""><td>0.70</td><td>2.75</td><td>0.59</td><td><lor< td=""><td>2.13</td><td><lor< td=""><td>45.59</td><td>0.06</td><td>1.00</td><td>2.79</td><td>5.21</td></lor<></td></lor<></td></lor<>	0.70	2.75	0.59	<lor< td=""><td>2.13</td><td><lor< td=""><td>45.59</td><td>0.06</td><td>1.00</td><td>2.79</td><td>5.21</td></lor<></td></lor<>	2.13	<lor< td=""><td>45.59</td><td>0.06</td><td>1.00</td><td>2.79</td><td>5.21</td></lor<>	45.59	0.06	1.00	2.79	5.21
	WQO of TIN: 0.5 mg/L													5 mg/L
	Wet Season WQO of SS : 11.0 mg/l													0 mg/L

Notes:

Cell shaded yellow / red indicate value exceeding the Action/Limit levels.

Cell shaded grey indicate value exceeding the WQO.

Cell shaded grey indicate value exceeding the WQO.


Annex C


Dredging Record for ESC CMP Vb


Date	Daily Dredging Volume (m ³)	Weekly Dredging Volume (m ³) (From Sunday to Saturday)
01-Jul-2017	0	0
02-Jul-2017	0	
03-Jul-2017	0	
04-Jul-2017	0	
05-Jul-2017	0	0
06-Jul-2017	0	
07-Jul-2017	0	
08-Jul-2017	0	
09-Jul-2017	0	
10-Jul-2017	0	
11-Jul-2017	0	1
12-Jul-2017	0	0
13-Jul-2017	0	
14-Jul-2017	0	1
15-Jul-2017	0	1
16-Jul-2017	0	
17-Jul-2017	0	1
18-Jul-2017	0	1
19-Jul-2017	0	0
20-Jul-2017	0	1
21-Jul-2017	0	
22-Jul-2017	0	
23-Jul-2017	0	
24-Jul-2017	0	
25-Jul-2017	0	1
26-Jul-2017	0	500
27-Jul-2017	0	1
28-Jul-2017	0	1
29-Jul-2017	500	1
30-Jul-2017	2,000	4.500
31-Jul-2017	2,500	4,500


Annex D


Graphical Presentations

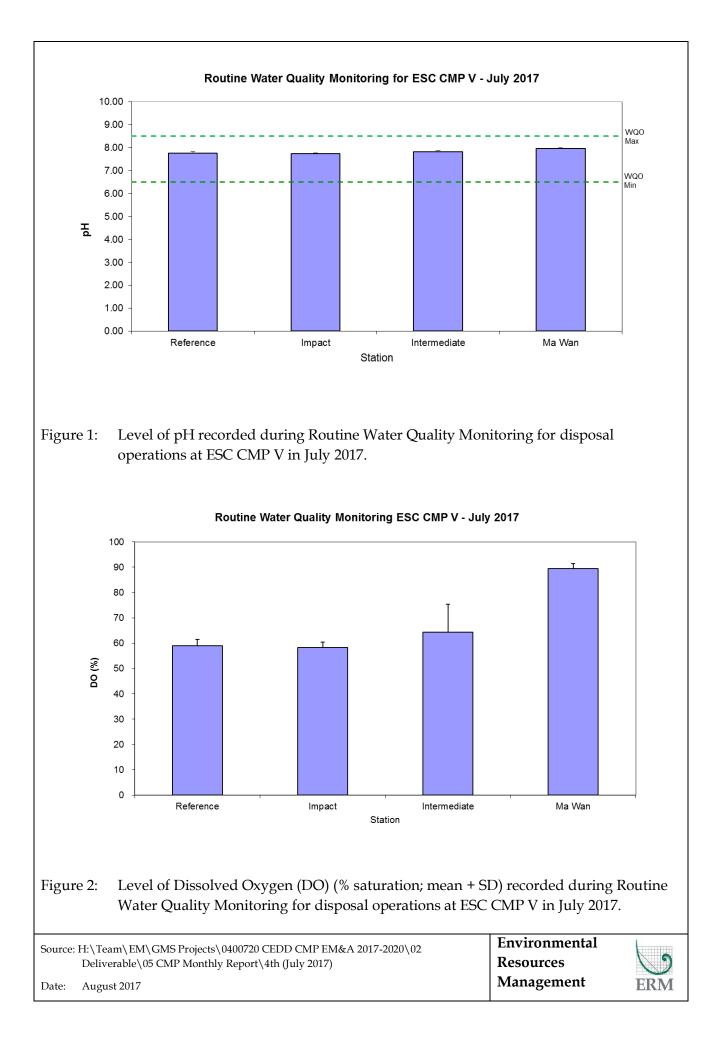


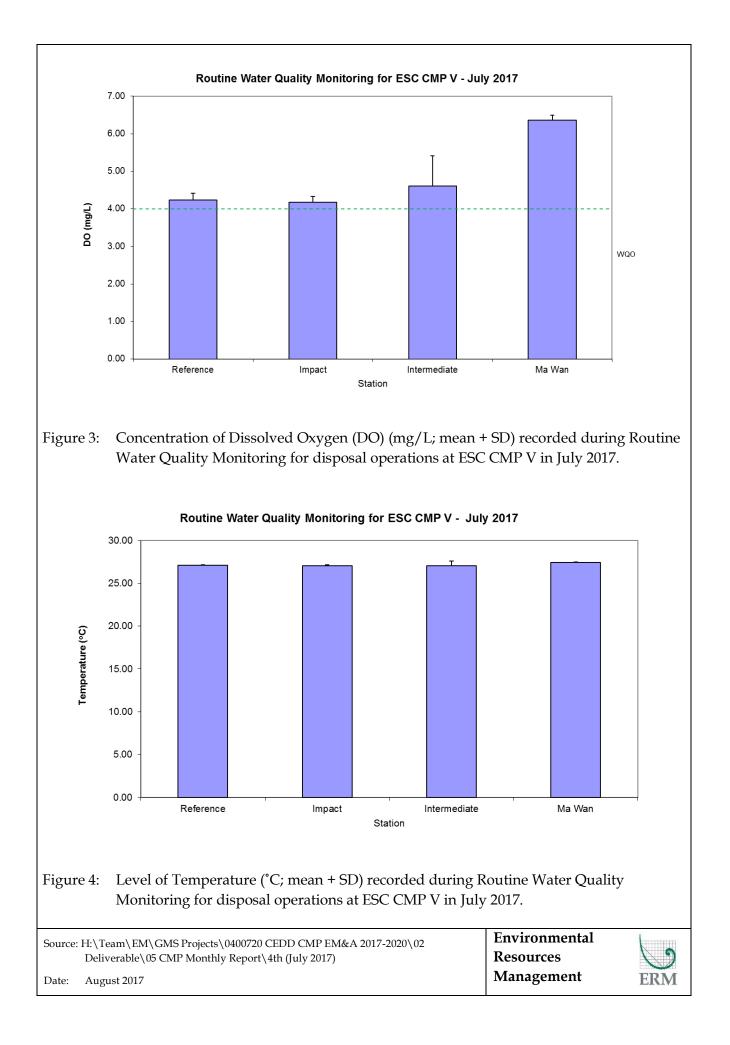


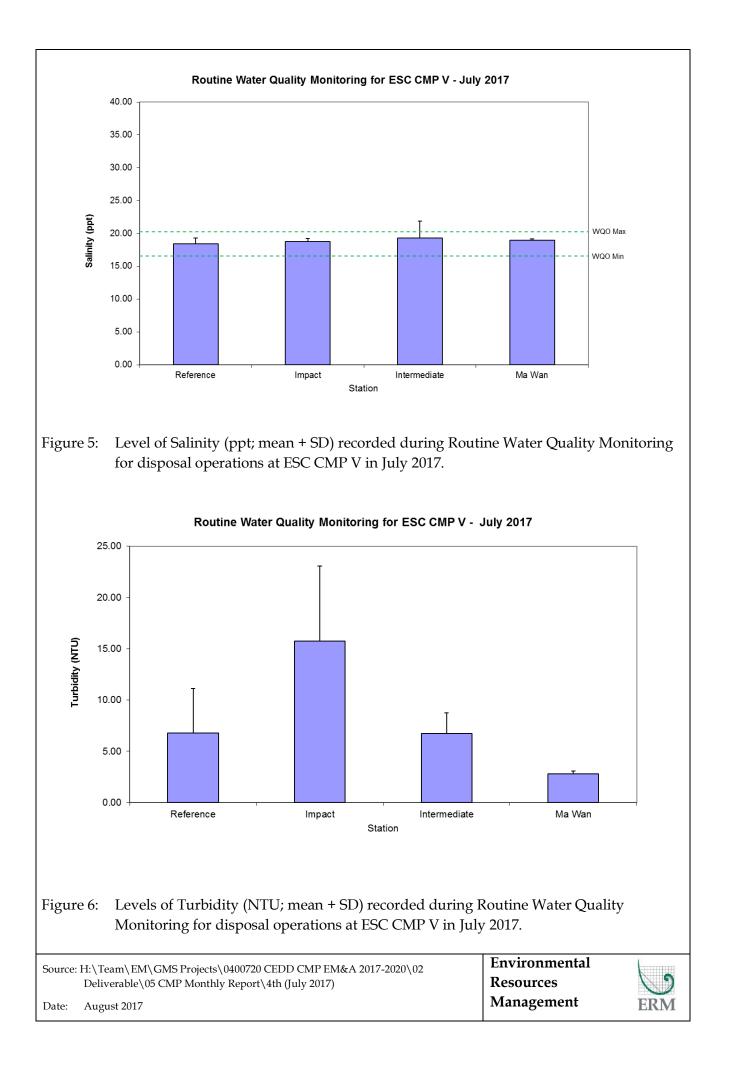


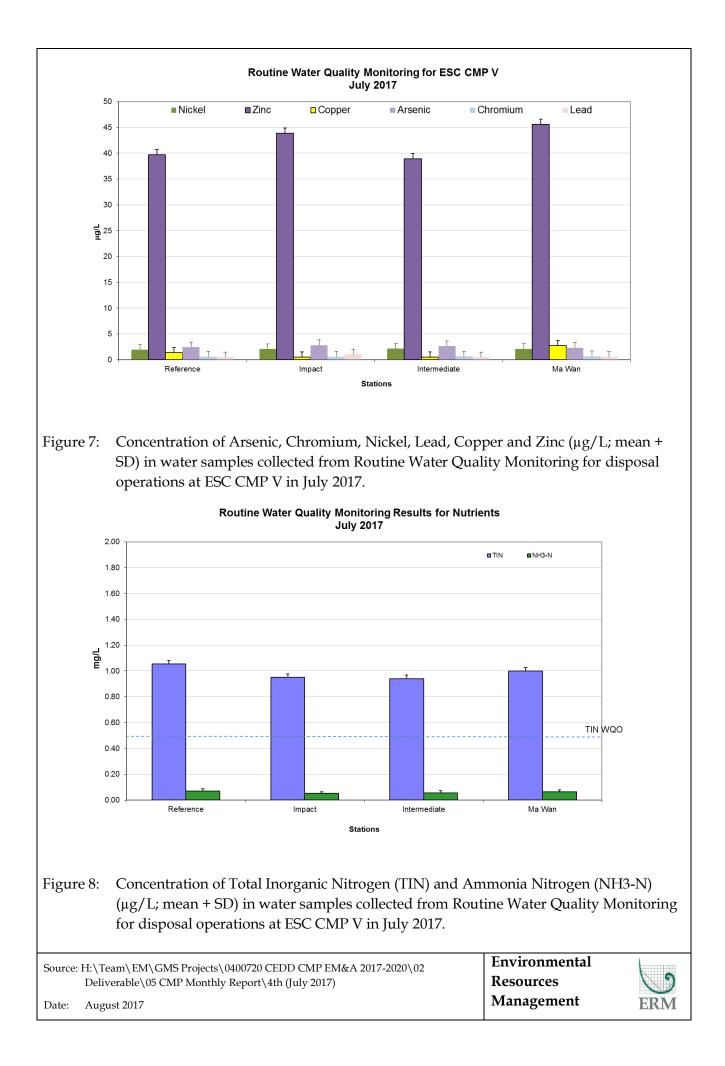


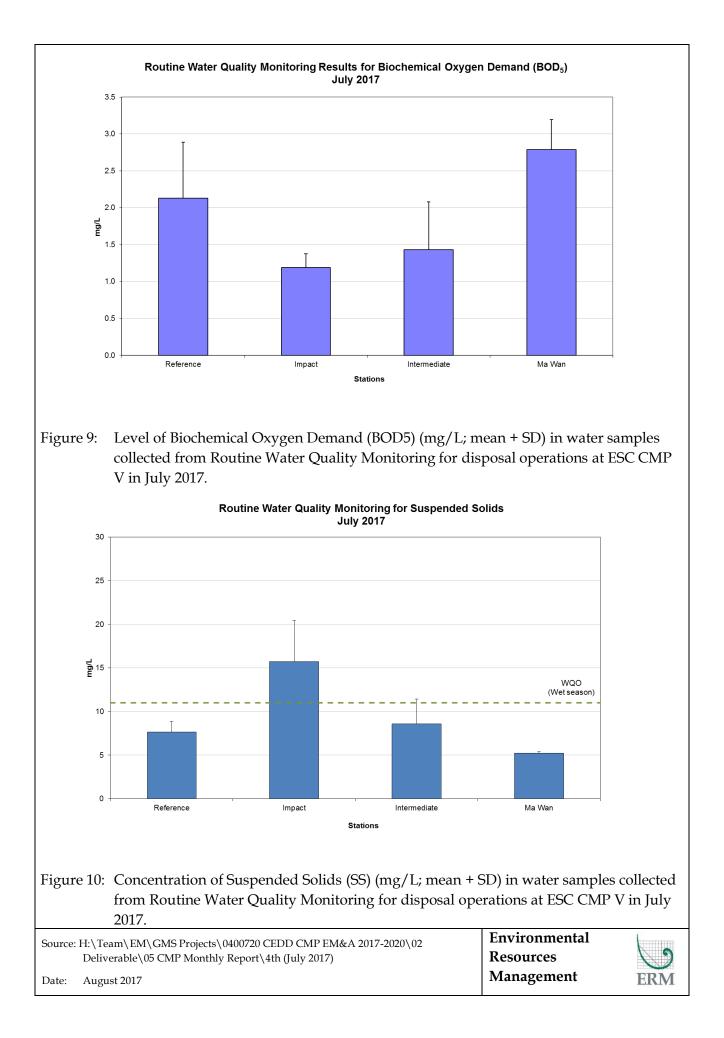

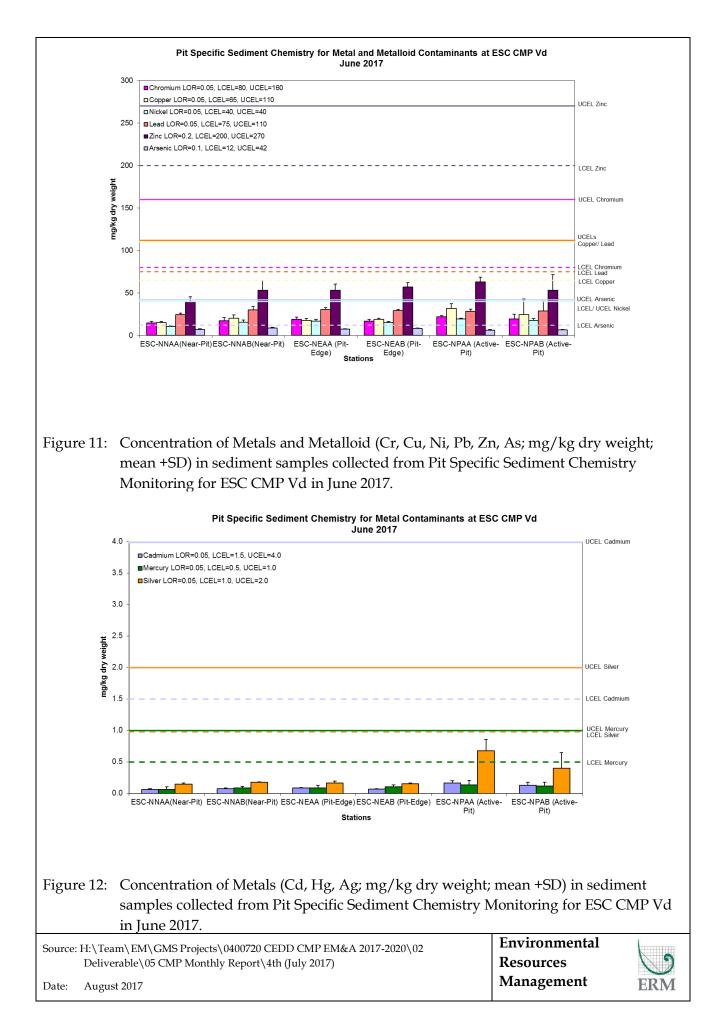

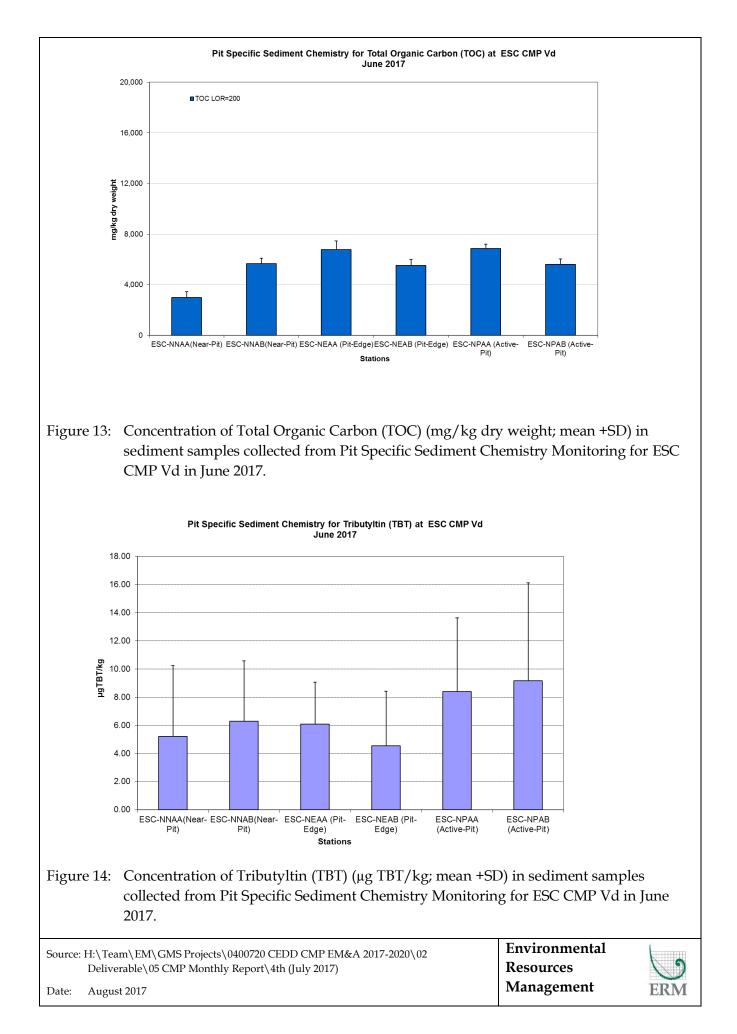

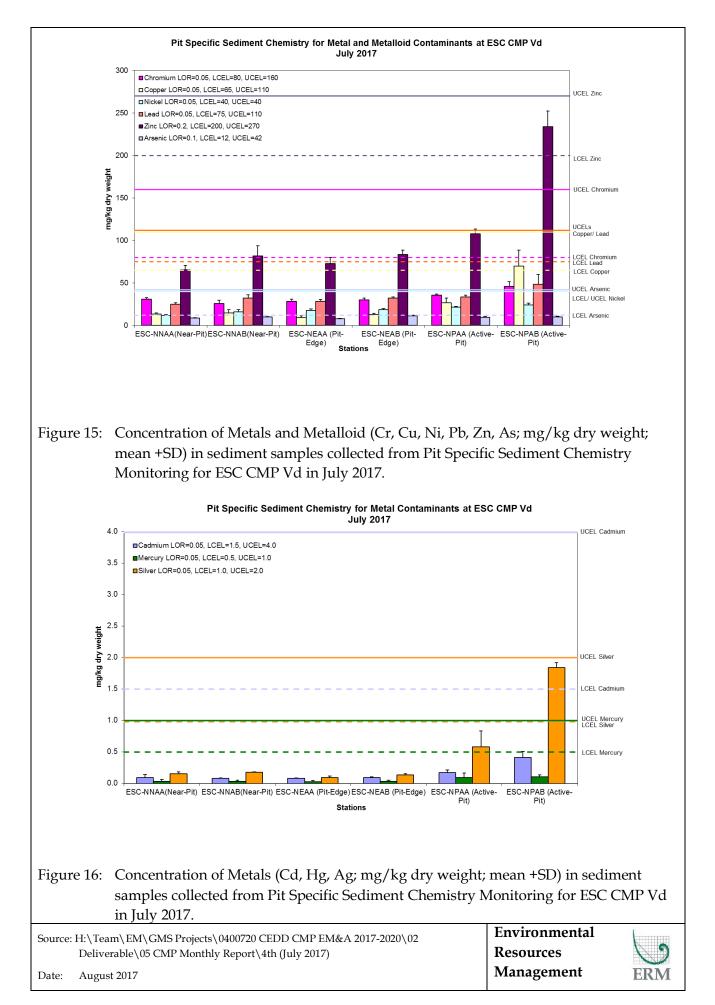

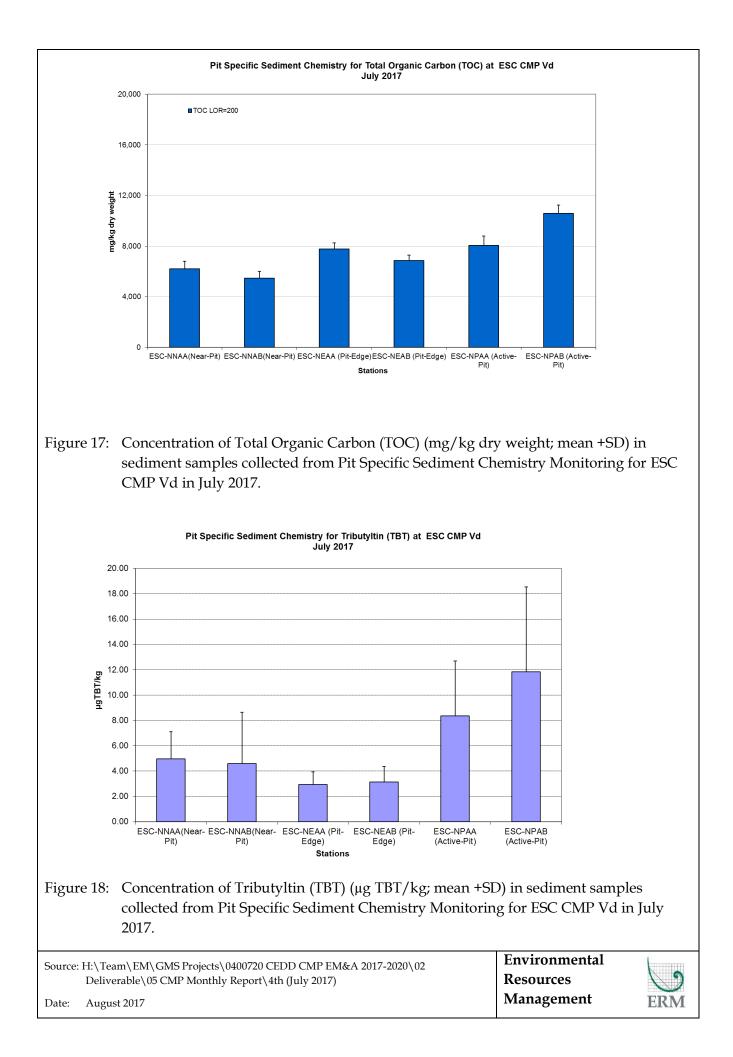




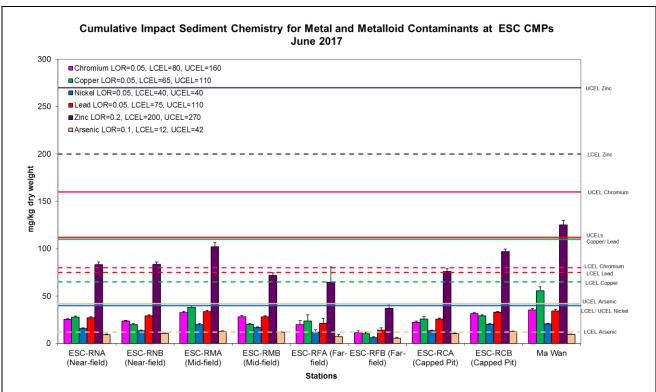


Figure 19: Concentration of Metals and Metalloid (Cr, Cu, Ni, Pb, Zn, As; mean +SD) in sediment samples collected from Cumulative Impact Sediment Chemistry Monitoring for ESC CMPs in June 2017.

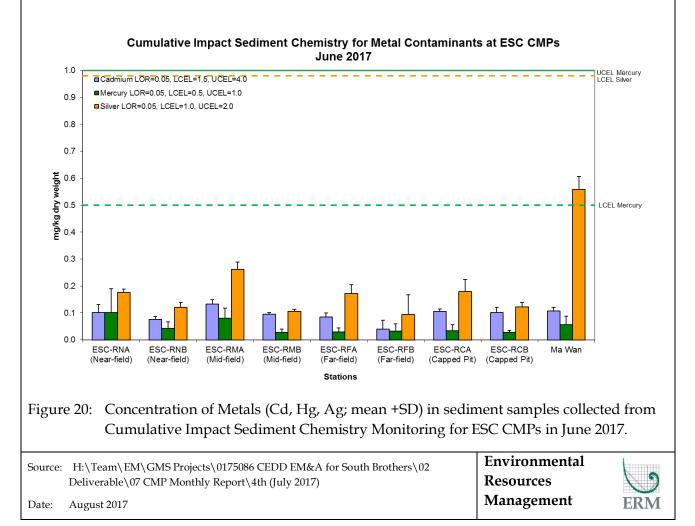

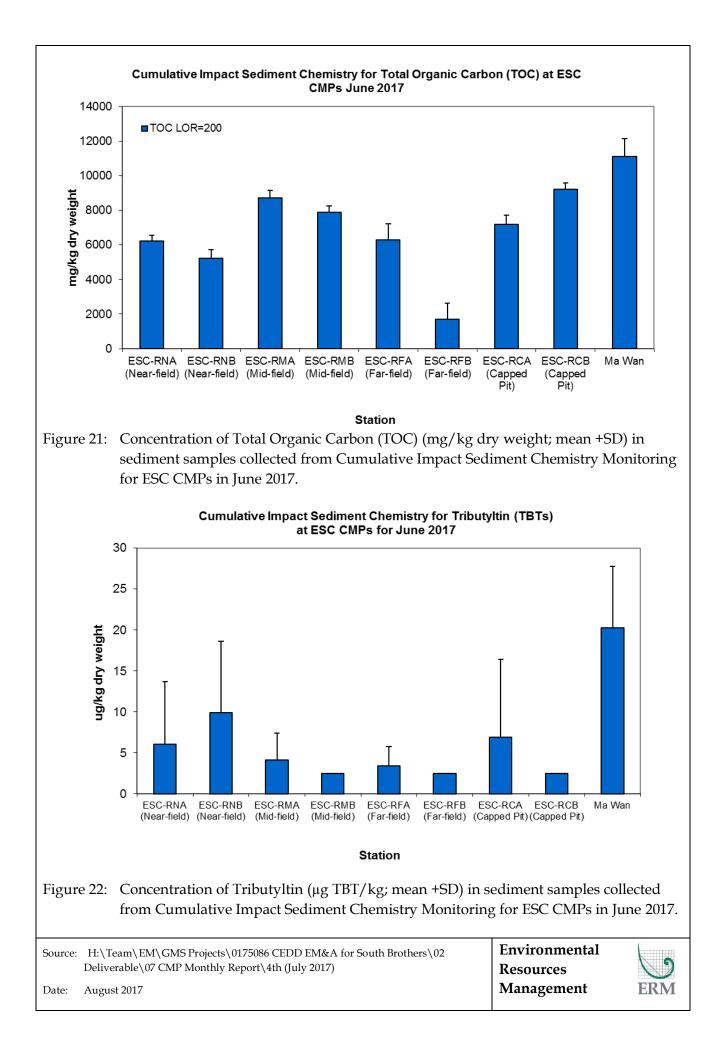

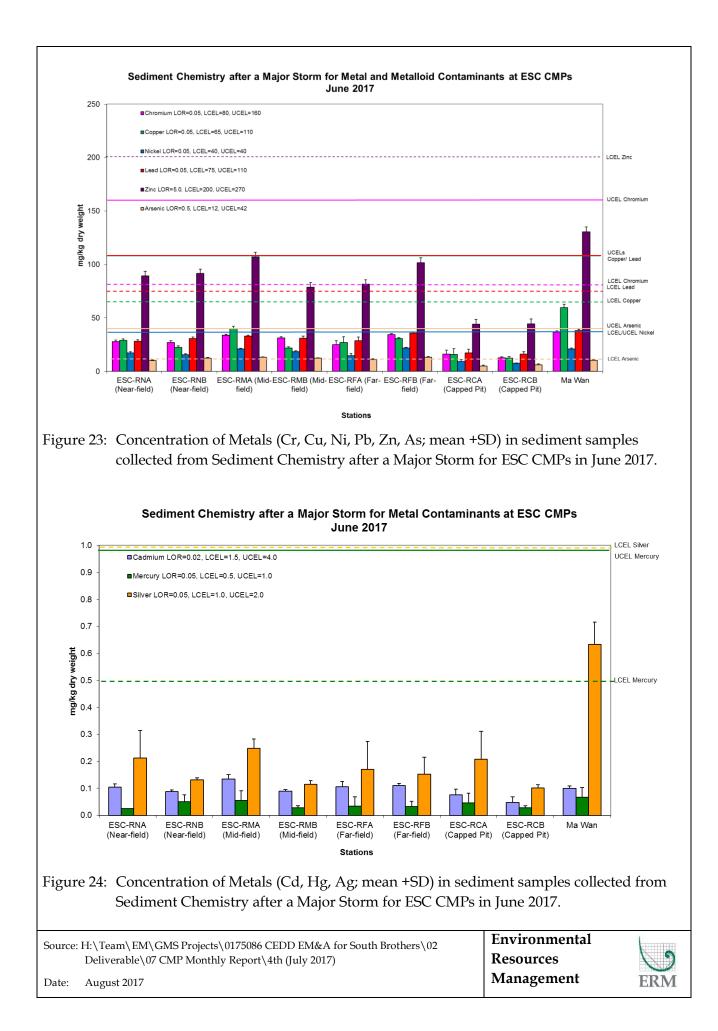

Annex E

Study Programme

Task Name		Finish		201	7				2018	3				2019				2	020			JFMA	202	21		Ξ
Commencement of Agreement No. CE 63/2016 (EP)	Sat 1/4/17	Sat 1/4/17			JAS		JJF	MA	MJJ	ASC		JFI		JJ	ASO	ND	JFM	AM.	JJA	SON	4DJ	FMA	1 M J	JAS)]
																			\square			+++			\square	
	Nov 0/4/47	Mar 5/4/04																							\square	
Project Management and General Deliverables	Mon 3/4/17	Mon 5/4/21																	\square		Π		111			
For the disposal facilities to the East of Sha Chau (ESC) (between 2017 and 2021)	Sat 1/4/17	Fri 1/10/21	i 🐳																+++		÷	╪╤╤	+++		╞┼┼	
and the South of The Brothers (SB) (between 2017 and 2018)																										
Draft Report on Review of EM&A Manual	Tue 2/5/17	Tue 2/5/17		2/5																						
Final Report on Review of EM&A Manual	Tue 23/5/17	Tue 23/5/17	$\left \cdot \right $	23	3/5											_		$\left \right $	++	\square	+	+++	+++	++	\vdash	++
Regular Review of EM&A Manual	Wed 2/5/18	Sat 2/5/20							>									\diamond								
Regular Site Inspections of CMP Contractors	Sat 1/4/17	Wed 31/3/21																								
Derticipate in Linian Occurs Martiner / Occurs Matines on required by OCDD	Sat 1/4/17	Wed 31/3/21																					+++	++	\square	\square
Participate in Liaison Group Meetings/ Consultations as required by CEDD	Sat 1/4/17	Weu 31/3/21																	T							
Submission of Monthly EM&A Report	Sun 14/5/17	Sun 14/3/21		>�	00		> <		$\diamond \diamond$	$\diamond \diamond$	$\diamond \diamond$	~		\diamond	>>	$\diamond \diamond$	$\diamond \diamond$		> 0		\$¢	$\Diamond \Diamond$				
Submission of Quarterly EM&A Report	Fri 14/7/17	Wed 14/4/21	$\left \right $		>	\diamond					>		\diamond					\diamond	\diamond	\diamond	++		<u></u>	++	\vdash	++
						Ň							Ň					Ň	Ň							
Submission of Annual EM&A Report	Sun 14/1/18	Thu 14/1/21					\diamond					\diamond					\diamond					>				
Submission of Annual Risk Assessment Report	Thu 14/6/18	Mon 14/6/21							\diamond					\diamond		_			>	\square	++	+++	\diamond	++	\vdash	+
	Er: 00/7/04	Eri 00/7/01																				+++	+++	¢_23/		\square
Submission of Draft Final Report (including database of all data collected)	Fri 23/7/21	Fri 23/7/21																							1	
Submission of Final Report (including database of all data collected)	Fri 27/8/21	Fri 27/8/21																							27/8	T
Submission of Draft Executive Summary	Fri 27/8/21	Fri 27/8/21	$\left \cdot \right $			$\left \right $				$\left \right $	++		++	$\left \cdot \right $	+			$\left \right $	++-	++	++-	+++	+++	-	27/8	++
Submission of Dran Excedure Summary																										
Submission of Final Executive Summary	Fri 1/10/21	Fri 1/10/21																							1/10	2
			$\left \right $						++-		++		++		++	_		\vdash	++	\square	++	+++	+++	++	\vdash	+
For East Tung Lung Chau Disposal Facility (subject to the actual disposal	Sun 14/10/18	Fri 14/12/18	$\left \right $													_		$\left \right $	++	\square	++	+++	+++	++	H	++
programme to be confirmed by CEDD)																										
Submission of Monthly EM&A Report		Fri 14/12/18									>00								++-							T
Submission of Quarterly EM&A Report		Fri 14/12/18										14/1	2					\square	++	\square	++	+++	+++		\square	
		111 14/12/10											2													
Submission of Annual EM&A Report	Fri 14/12/18	Fri 14/12/18									•	14/1	2													
Study Programme Task Milestone	•	S	Summa	ary						F F	Rolled	Up M	ilesto	ne 🛇												
Tue 13/6/17				<u> </u>						-																
Agreement No. CE 63/2016 (EP) Environmenta	al Monitoring a	nd Audit for Di	spos	al Fa	acilit	y to t	he E	ast o	of Sha	a Cha	iu (20	17-2	020)	- Inv	estiga	atior	י ו)4007	20_C	MP EN	M&A	Progra	amme_	_v1_E	Л&А.m	npp
