土木工程拓展署
Civil Engineering and Development Department

Agreement No. CE 63/2016 (EP)

Environmental Monitoring and Audit for Disposal Facility to the East of Sha Chau (2017-2020) – Investigation

Monthly EM&A Report for Contaminated Mud Pits to the East of Sha Chau – July 2020

Revision 0

August 2020

Environmental Resources Management
2507, 25/F, One Harbourfront
18 Tak Fung Street
Hunghom, Kowloon
Hong Kong
Telephone (852) 2271 3000
Facsimile (852) 2723 5660

www.erm.com

ERM

The business of sustainability

Agreement No. CE 63/2016 (EP) Environmental Monitoring and Audit for Disposal Facility to the East of Sha Chau (2017-2020) – Investigation

Monthly EM&A Report for Contaminated Mud Pits to the East of Sha Chau – July 2020

Revision 0

Document Code: 0400720_Monthly July 2020_v0.doc

Environmental Resources Management

2507, 25/F, One Harbourfront
18 Tak Fung Street
Hunghom, Kowloon
Hong Kong
Telephone: (852) 2271 3000
Facsimile: (852) 2723 5660
E-mail: post.hk@erm.com
http://www.erm.com

Client: Civil Engineering and Development Department (CEDD)	Project No: 0400720
Summary: This document presents the Monthly EM&A Report for *Environmental Monitoring and Audit for Disposal Facility to the East of Sha Chau*.	Date: 10 August 2020 Approved by:  Craig A. Reid *Partner*

Revision	Description	By	Checked	Approved	Date
v0	Monthly EM&A Report for ESC CMPs	GS	RC	CAR	10/08/20

Distribution

☐ Internal

☒ Public

☐ Confidential

OHSAS 18001:2007
Certificate No. OHS 515956

ISO 9001 : 2008
Certificate No. FS 32515

土木工程拓展署
Civil Engineering and Development Department

ERM

Dredging, Management and Capping of Contaminated Sediment Disposal Facility at Sha Chau

Environmental Certification Sheet
EP-312/2008/A

Reference Document/Plan

Document/~~Plan~~ to be ~~Certified~~/ Verified:	Monthly EM&A Report for Contaminated Mud Pits to the East of Sha Chau – July 2020
Date of Report:	10 August 2020
Date prepared by ET:	10 August 2020
Date received by IA:	10 August 2020

Reference EP Condition

Environmental Permit Condition:

Condition 3.4 of EP-312/2008/A:
4 hard copies and 1 electronic copy of monthly EM&A Report shall be submitted to the Director within 2 weeks after the end of the reporting month. The EM&A Reports shall include a summary of all non-compliance (exceedances) of the environmental quality performance limits (Action and Limit Levels). The submissions shall be certified by the ET Leader and verified by the Independent Auditor. Additional copies of the submission shall be provided to the Director upon request by the Director.

ET Certification

I hereby certify that the above referenced document/~~plan~~ complies with the above referenced condition of EP-312/2008/A

Craig Reid,
Environmental Team Leader:  Date: 10/08/2020

IA Verification

I hereby verify that the above referenced document/~~plan~~ complies with the above referenced condition of EP-312/2008/A

Dr Wang Wen Xiong,
Independent Auditor:  Date: 10/08/2020

CONTENTS

ANNEXES

Agreement No. CE 63/2016 (EP)
Environmental Monitoring and Audit
for Disposal Facility to the East of Sha Chau (2017-2020) - Investigation

MONTHLY EM&A REPORT FOR JULY 2020

1.1 BACKGROUND

1.1.1 The Civil Engineering and Development Department (CEDD) is managing a number of marine disposal facilities in Hong Kong waters, including the Contaminated Mud Pits (CMPs) to the South of The Brothers (SB) and to the East of Sha Chau (ESC) for the disposal of contaminated sediment, and open-sea disposal grounds located to the South of Cheung Chau (SCC), East of Tung Lung Chau (ETLC) and East of Ninepins (ENP) for the disposal of uncontaminated sediment. Two Environmental Permits (EPs), EP-312/2008/A and EP-427/2011/A, were issued by the Environmental Protection Department (EPD) to the CEDD, the Permit Holder, on 28 November 2008 and 23 December 2011 for the Dredging, Management and Capping of Contaminated Sediment Disposal Facilities at ESC CMP V and SB CMPs, respectively.

1.1.2 Under the requirements of the two EPs for ESC CMP V and SB CMPs, EM&A programmes which encompass water and sediment chemistry, fisheries assessment, tissue and whole body analysis, sediment toxicity and benthic recolonisation studies as set out in the EM&A Manuals are required to be implemented. EM&A programmes have been continuously carried out during the operation of the CMPs at ESC and SB. A review of the collection and analysis of such environmental data from the monitoring programme demonstrated that there had not been any adverse environmental impacts resulting from disposal activities (1) (2). The current programme will assess the impacts resulting from dredging, disposal and capping operations of CMP V as well as capping operations of SB CMPs.

1.1.3 The present EM&A programme under *Agreement No. CE 63/2016 (EP)* covers the dredging, disposal and capping operations of the ESC CMP V as well as the capping operations of the SB CMPs (see *Annex A* for the EM&A programme). The scheduled EM&A programme for SB CMPs was completed in December 2018. Detailed works schedule for ESC CMP V is shown in *Figure 1.1*. In July 2020, the following works were undertaken:

- Disposal of contaminated mud at ESC CMP Vb; and
- Capping operations at ESC CMP Vd.

(1) ERM (2013) Final Report. Submitted under Agreement No. CE 4/2009 (EP) Environmental Monitoring and Audit for Contaminated Mud Pit at East Sha Chau. For CEDD.

(2) ERM (2017) Final Report. Submitted under Agreement No. CE 23/2012 (EP) Environmental Monitoring and Audit for Contaminated Mud Pits to the South of The Brothers and at East Sha Chau (2012 - 2017). For CEDD.

Figure 1.1 Works Schedule for ESC CMP V



1.2 REPORTING PERIOD

1.2.1 This *Monthly EM&A Report for July 2020* covers the EM&A activities for the reporting month of July 2020.

1.3 DETAILS OF SAMPLING AND LABORATORY TESTING ACTIVITIES

1.3.1 The following monitoring activities were undertaken for ESC CMP V in July 2020:

- *Water Column Profiling of ESC CMP Vb*;
- *Routine Water Quality Monitoring of ESC CMPs*;
- *Pit Specific Sediment Chemistry of ESC CMP Vb;* and
- *Demersal Trawling for ESC CMPs.*

1.4 DETAILS OF OUTSTANDING SAMPLING AND/OR ANALYSIS

1.4.1 No outstanding sampling remained for July 2020.

1.4.2 The following analyses are in progress and will be presented in the corresponding quarterly report:

- Species identification of the biota samples collected from *Demersal Trawling for ESC CMPs* in July 2020.

1.5 BRIEF DISCUSSION OF THE MONITORING RESULTS FOR ESC CMP V

1.5.1 Brief discussion of the monitoring results of the following activities for ESC CMP V is presented in this *Monthly EM&A Report for July 2020*:

- *Water Column Profiling of ESC CMP Vb*;
- *Routine Water Quality Monitoring of ESC CMPs;* and
- *Pit Specific Sediment Chemistry of ESC CMP Vd.*

1.5.2 ***Water Column Profiling of ESC CMP Vb – July 2020***

1.5.3 *Water Column Profiling* was undertaken at a total of two sampling stations (Upstream and Downstream stations) on 8 July 2020. The monitoring results have been assessed for compliance with the Water Quality Objectives (WQOs) set by Environmental Protection Department (EPD). This consists of a review of the EPD routine water quality monitoring data for the wet season period (April to October) of 2009 - 2018 from stations in the Northwestern Water Control Zone (WCZ), where the ESC CMPs are located [1]. For Salinity, the averaged value obtained from the Reference (Upstream) station was used for the basis as the WQO. Levels of Dissolved Oxygen (DO) and Turbidity were also assessed for compliance with the Action and Limit Levels (see *Table B1* of *Annex B* for details).

In-situ Measurements

1.5.4 Analyses of results for July 2020 indicated that levels of Salinity, pH and DO complied with the WQOs at both Downstream and Upstream stations (*Table B2* of *Annex B*). Levels of DO and Turbidity at all stations complied with the Action and Limit Levels (*Tables B1* and *B2* of *Annex B*).

Laboratory Measurements for Suspended Solids (SS)

1.5.5 Analyses of results July 2020 indicated that the SS levels at both Downstream and Upstream stations complied with the WQO and the Action and Limit Levels (*Tables B1* and *B2* of *Annex B*).

1.5.6 Overall, the monitoring results indicated that the mud disposal operation at ESC CMP Vb did not appear to cause any deterioration in water quality during this reporting period.

1.5.7 ***Routine Water Quality Monitoring of ESC CMPs – July 2020***

1.5.8 *Routine Water Quality Monitoring of ESC CMPs* was undertaken on 10 July 2020. The monitoring results have been assessed for compliance with the WQOs (see *Section 1.5.3* for details). The monitoring results are shown in *Tables B3 and B4* of *Annex B* and *Figures 1 - 10* of *Annex C*. A total of ten (10) monitoring stations were sampled in July 2020 as shown in *Figure 1.2*.

[1] http://epic.epd.gov.hk/EPICRIVER/marine/?lang=en

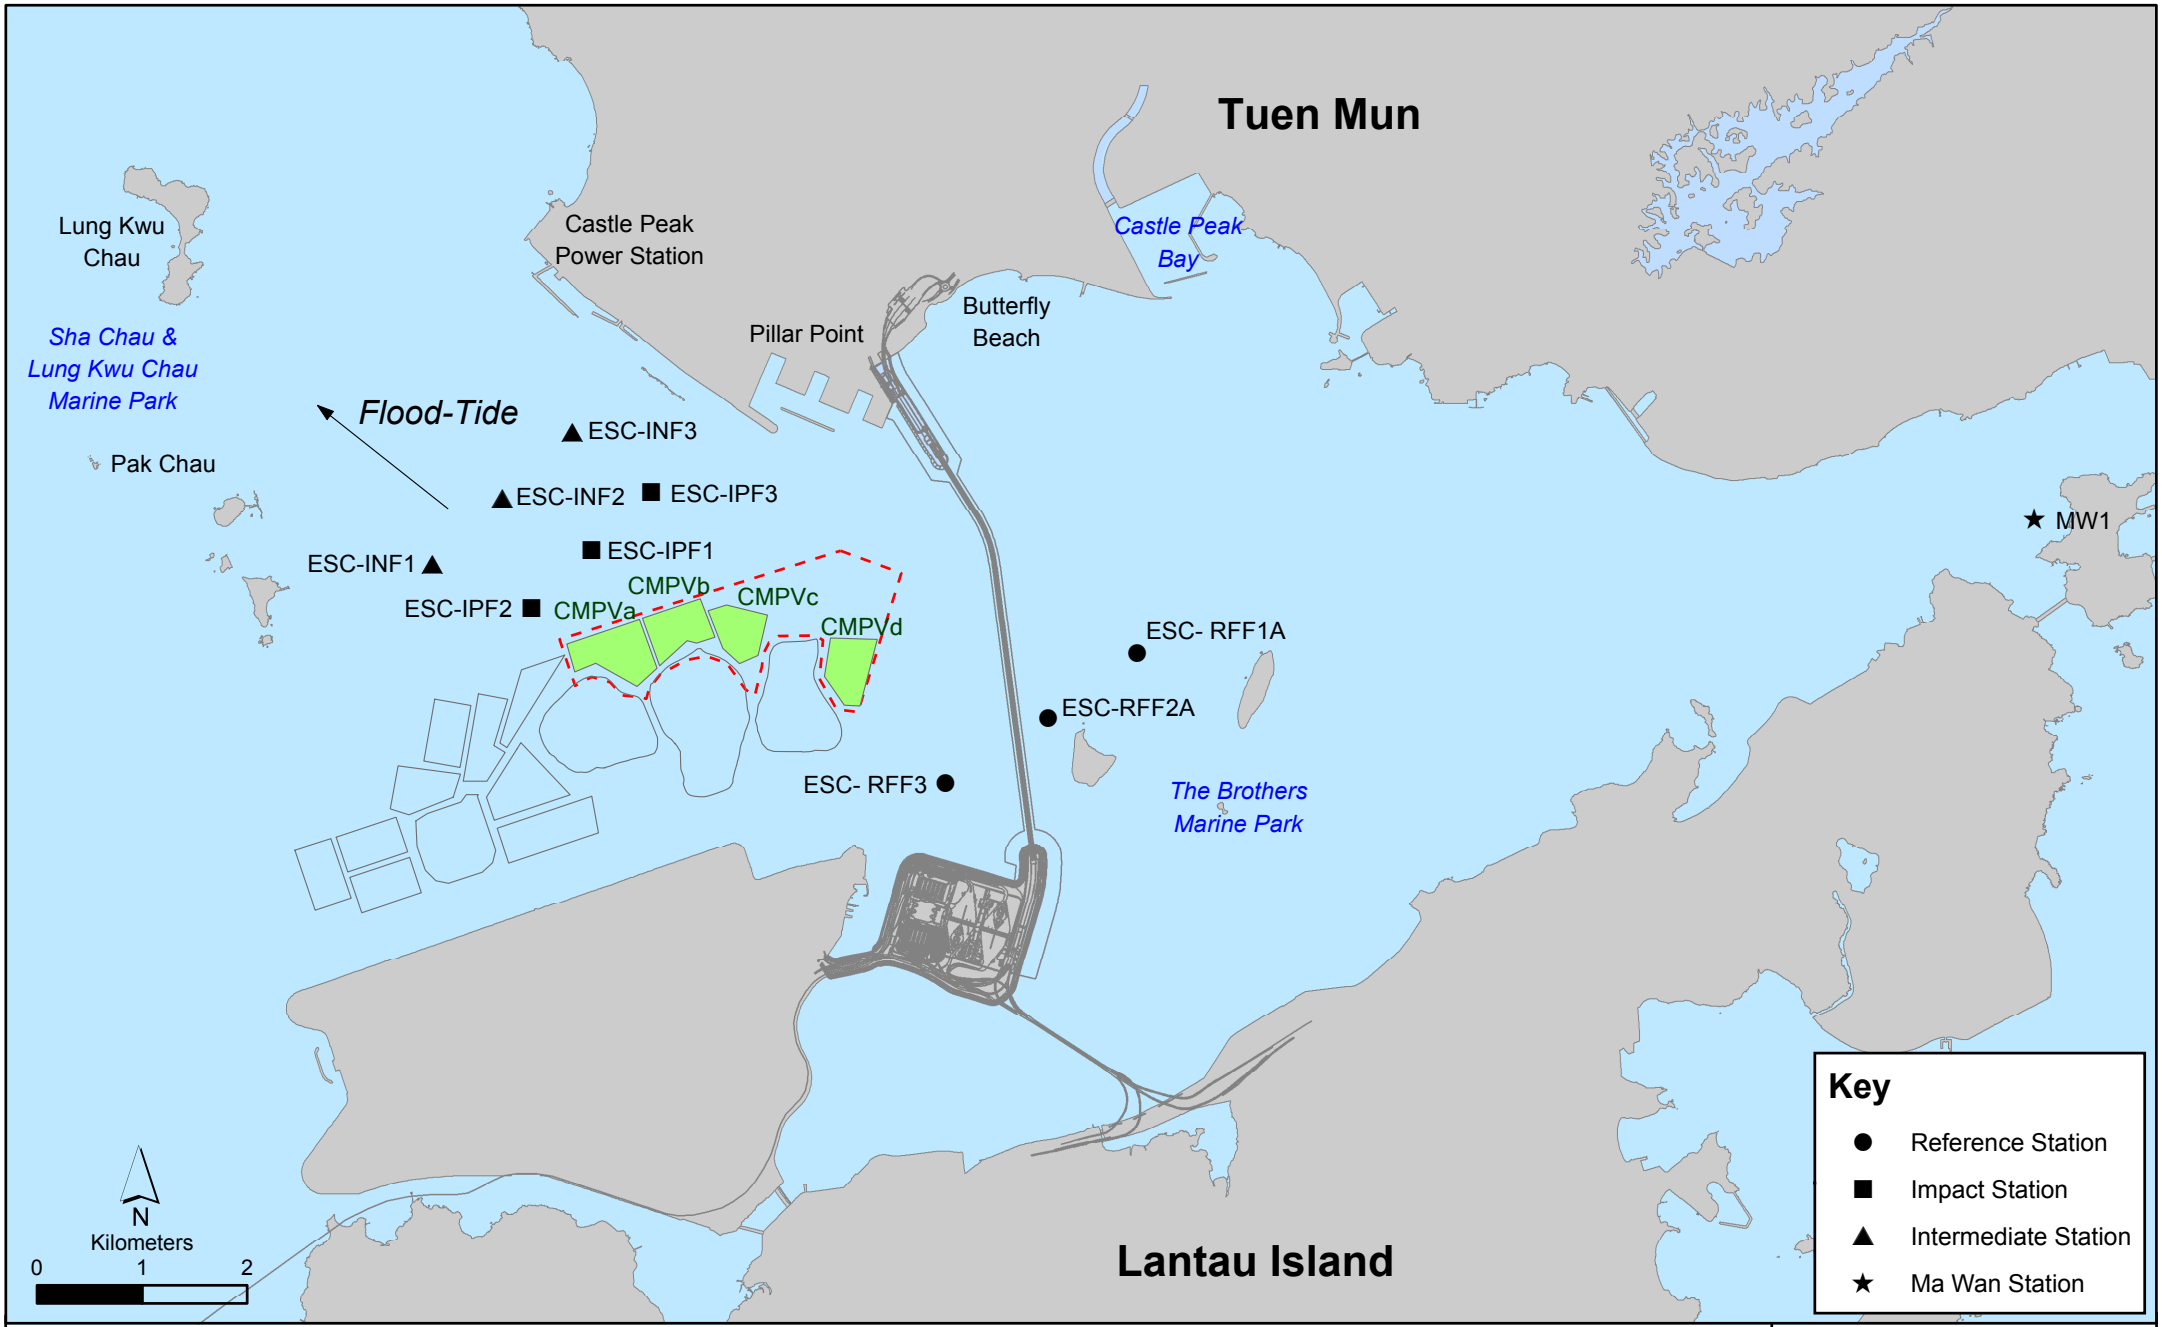

Figure 1.2

Routine & Capping Water Quality Sampling Stations (Flood-Tide) for ESC CMPs

File: T:\GIS\CONTRACT\0175086\Mxd\updated_20170419\0175086_R_C_WQMS_flood.mxd
Date: 25/4/2017

Environmental Resources Management

ERM

In-situ Measurements

1.5.9 Graphical presentation of the monitoring results (Temperature, DO, pH, Salinity and Turbidity) is shown in *Figures 1 - 6* of *Annex C*. Analyses of results for July 2020 indicated that the levels of pH, Salinity and DO complied with the WQOs at most stations in July 2020, except higher levels of salinity were recorded in Ma Wan station. The higher Salinities recorded at Ma Wan station are likely to be caused by the larger separation distance to Pearl River mouth, which release a large amount of freshwater runoff in the area during flooding, when compared to the Reference stations.

1.5.10 The levels of DO and Turbidity complied with the Action and Limit Levels at all stations (*Table B3* of *Annex B*; *Figures 3* and *6* of *Annex C*).

1.5.11 Overall, *in-situ* measurement results of the *Routine Water Quality Monitoring* indicated that the disposal operation at ESC CMP Vb did not appear to cause any unacceptable impacts in water quality in July 2020.

Laboratory Measurements

1.5.12 Laboratory analysis of July 2020 results indicated that concentrations of Arsenic, Chromium, Copper, Lead, Nickel and Zinc were detected in July 2020 samples at most stations and the concentrations of most metals and metalloids were similar amongst the stations, except the concentrations of Copper were higher at Impact and Intermediate stations, and the concentrations of Lead and Zinc were higher at Ma Wan Station when compared to other stations (*Table B4* of *Annex B*; *Figure 7* of *Annex C*).

1.5.13 For nutrients, concentrations of Total Inorganic Nitrogen (TIN) at all stations were higher than the WQO (0.5 mg/L) (*Table B4* of *Annex B*; *Figure 8* of *Annex C*). It should be noted that due to the effect of the Pearl River, the North Western WCZ has historically experienced higher levels of TIN [(1)]. Therefore, the exceedances of TIN WQO at these stations are unlikely to be caused by the disposal operation at ESC CMPs. The concentrations of Ammonia Nitrogen (NH_3-N) and 5-day Biochemical Oxygen Demand (BOD_5) were higher at Ma Wan station in July 2020 (*Table B4* of *Annex B*; *Figure 8 and 9* of *Annex C*).

1.5.14 Analyses of results for July 2020 indicated that the SS levels at all stations complied with the WQO, and the SS levels at all stations complied with the Action and Limit Levels (*Tables B1 and B4* of *Annex B*; *Figure 10* of *Annex C*). There is no evidence indicating any unacceptable environmental impacts to nearby water sensitive receivers as a result of the mud disposal operations at ESC CMPs in July 2020.

(1) http://www.epd.gov.hk/epd/misc/marine_quality/1986-2005/textonly/eng/index.htm

1.5.15 Overall, results of the Routine Water Quality Monitoring indicated that the disposal operation at ESC CMPs did not appear to cause any unacceptable deterioration in water quality in July 2020. Detailed statistical analysis will be presented in the Quarterly Report to investigate any spatial and temporal trends of potential concern.

1.5.16 ***Pit Specific Sediment Chemistry of ESC CMP Vb – July 2020***

1.5.17 Monitoring locations for *Pit Specific Sediment Chemistry for ESC CMP Vb* are shown in *Figure 1.3.* A total of six (6) monitoring stations were sampled on 7 July 2020.

1.5.18 The concentrations of most inorganic contaminants were lower than the Lower Chemical Exceedance Levels (LCELs) at most stations, except for Arsenic (*Figures 11 and 12* of *Annex C*). The concentrations of Arsenic were higher than the LCEL at Pit-Edge station ESC-NECA and Active-Pit station ESC-NPCB.

1.5.19 Whilst the average concentration of Arsenic in the Earth's crust is generally ~2mg/kg, significantly higher Arsenic concentrations (median = 14 mg/kg) have been recorded in Hong Kong's onshore sediments [(1)]. It is presumed that the natural concentrations of Arsenic are similar in onshore and offshore sediments [(2)], and relatively high Arsenic levels may thus occur throughout Hong Kong. Therefore, the LECL exceedances of Arsenic are unlikely to be caused by the disposal operations at ESC CMP Vb but rather as a result of naturally occurring deposits.

1.5.20 For organic contaminants, the concentrations of Total Organic Carbon (TOC) were higher at Active-Pit stations ESC-NPCA and ESC-NPCB in July 2020 (*Figure 13 of Annex C*). The concentrations of Low Molecular Weight and High Molecular Weight Polycyclic Aromatic Hydrocarbons (PAHs) were lower than the LCELs at all stations (*Figure 14 of Annex C)*. The concentrations of Tributyltin (TBT) , Total Polychlorinated Biphenyls (PCBs), Total dichloro-diphenyl-trichloroethane (DDT) and 4,4'-dichlorodiphenyldichloroethylene (DDE) were below the limit of reporting at all stations in July 2020.

1.5.21 Overall, there is no evidence indicating any unacceptable environmental impacts to sediment quality as a result of the contaminated mud disposal operations at ESC CMP Vb in July 2020. Statistical analysis will be undertaken and presented in the corresponding quarterly report to investigate whether there are any unacceptable impacts in the area caused by the contaminated mud disposal.

(1) Sewell RJ (1999) Geochemical Atlas of Hong Kong. Geotechnical Engineering Office, Government of the Hong Kong Special Administrative Region

(2) Whiteside PGD (2000) Natural geochemistry and contamination of marine sediments in Hong Kong. In: The Urban Geology of Hong Kong (ed Page A & Reels SJ). Geological Society of Hong Kong Bulletin No. 6, p109-121

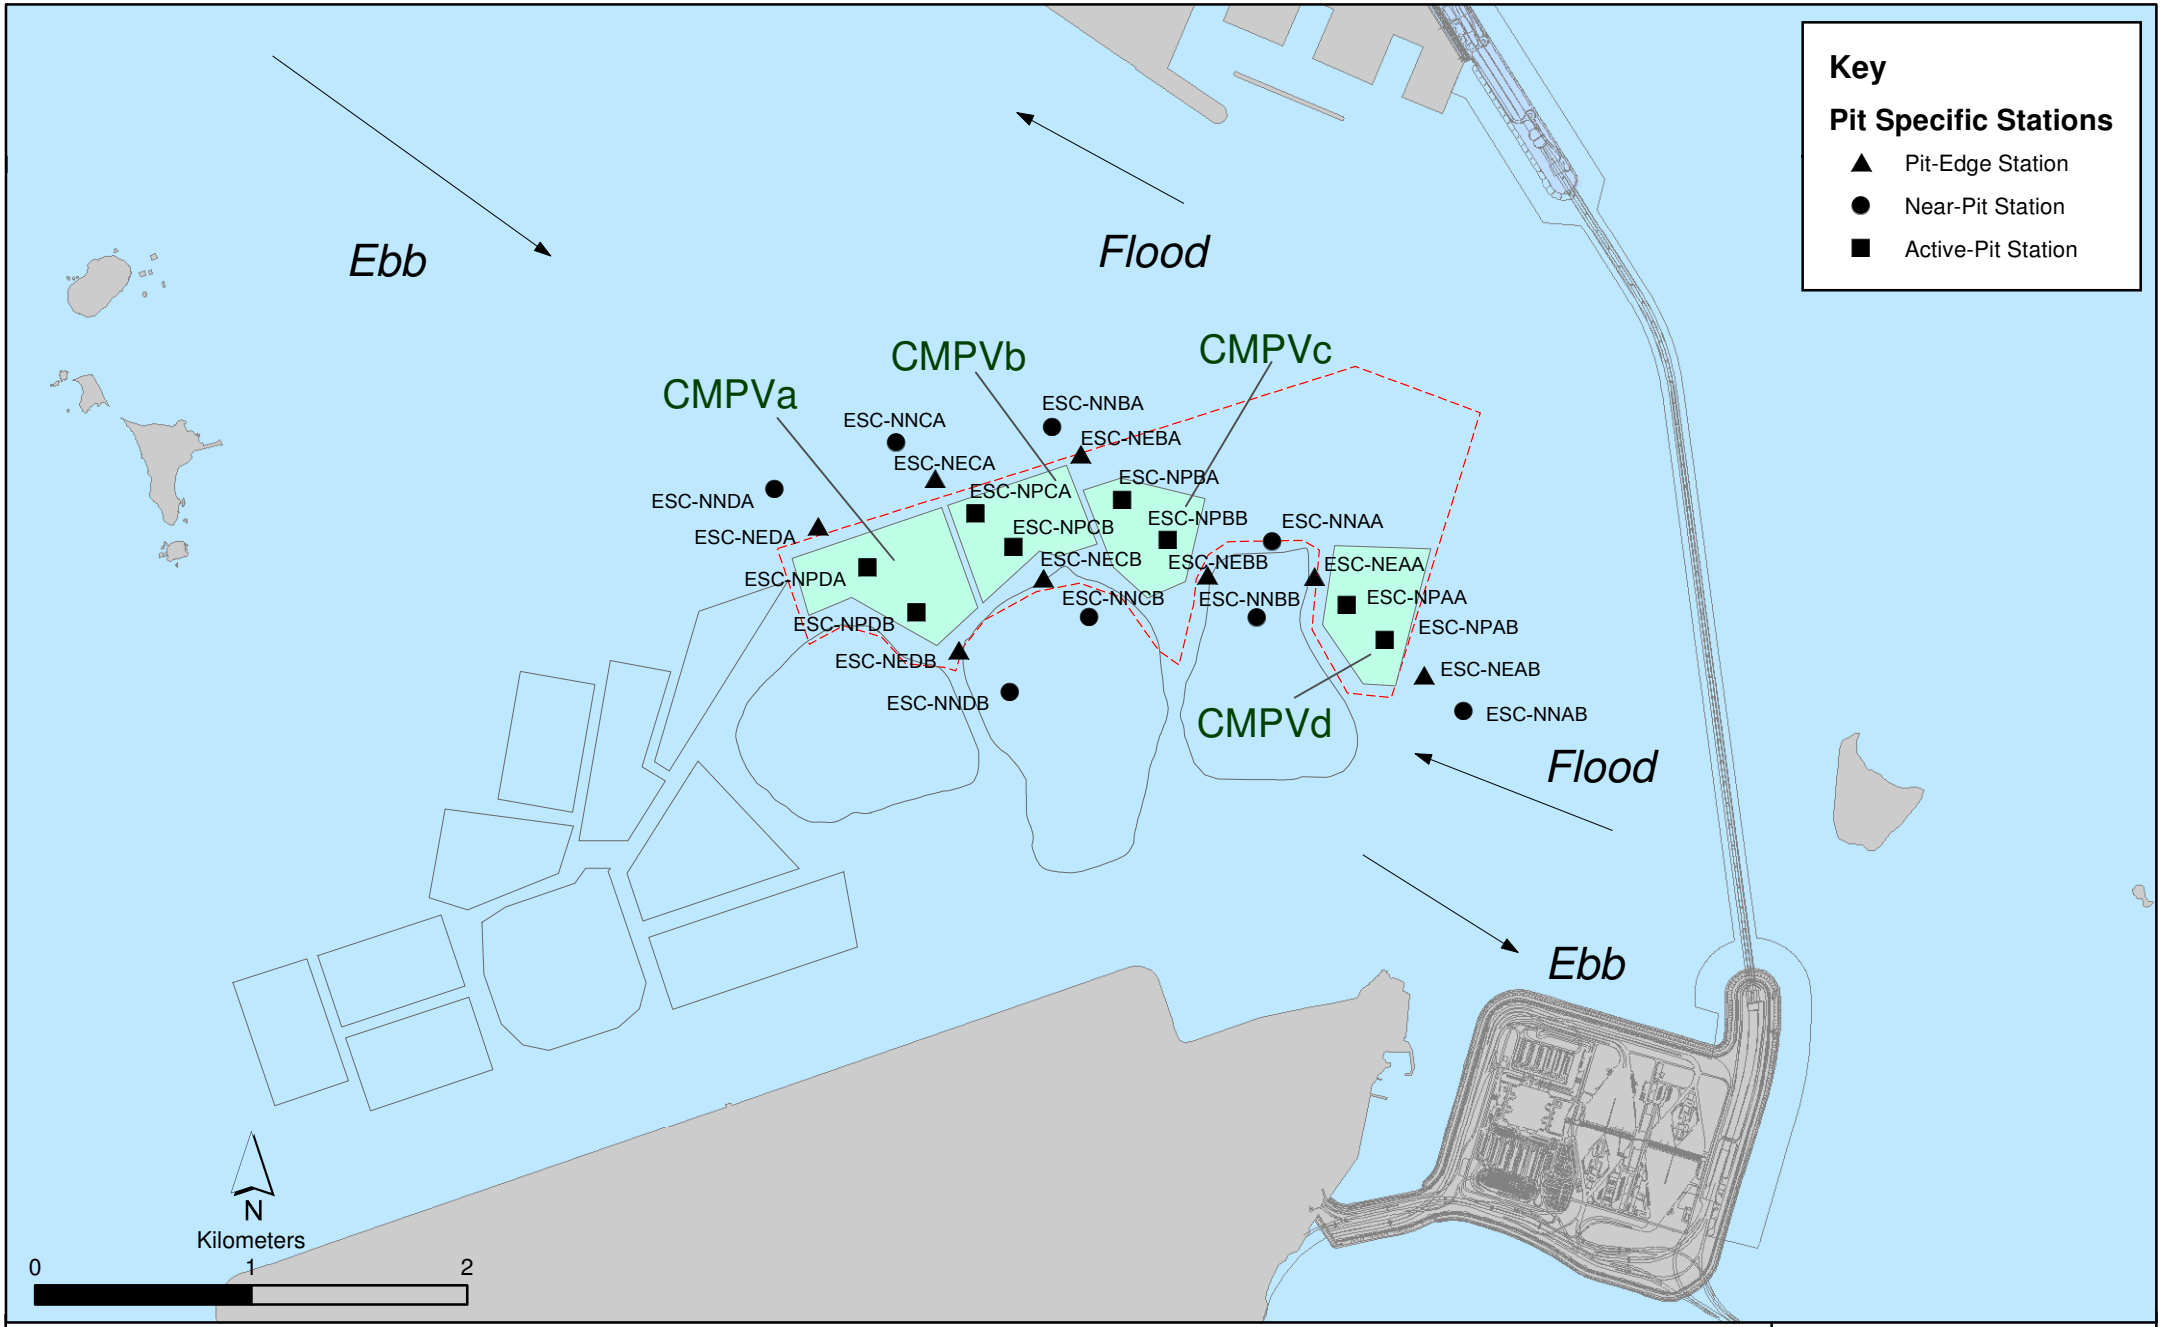

Figure 1.3

Pit Specific Sediment Quality Monitoring Stations for CMPV

File: T:\GIS\CONTRACT\0400720\Mxd\0400720_SQMS_pit specific.mxd
Date: 9/5/2017

Environmental Resources Management

ERM

1.6 ACTIVITIES SCHEDULED FOR THE NEXT MONTH

1.6.1 The following monitoring activities will be conducted in the next monthly period of August 2020 for ESC CMP V (see *Annex A* for the sampling schedule [1]):

- *Water Column Profiling of ESC CMP Vb*;
- *Routine Water Quality Monitoring of ESC CMPs*;
- *Pit Specific Sediment Chemistry of ESC CMP Vb;*
- *Cumulative Impact Sediment Chemistry of ESC CMP V;*
- *Sediment Toxicity Tests of ESC CMP V;*
- *Demersal Trawling for ESC CMPs;* and
- *Water Quality Monitoring During Capping of ESC CMPs*.

1.7 STUDY PROGRAMME

1.7.1 A summary of the Study Programme is presented in *Annex D*.

[1] The scheduled EM&A Programme for SB CMPs was completed in December 2018.

Annex A

Sampling Schedule

Annex A1 - East of Sha Chau Environmental Monitoring and Audit Sampling Schedule for CMP (April 2017 - March 2021)

			2017									2018												2019												2020												2021		
Pit Specific Sediment Chemistry	**Code**	**Frequency**	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
Active-Pit																																																		
	ESC-NPAA	Monthly	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12
	ESC-NPAB	Monthly	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12
Pit-Edge																																																		
	ESC-NEAA	Monthly	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12
	ESC-NEAB	Monthly	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12
Near-Pit																																																		
	ESC-NNAA	Monthly	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12
	ESC-NNAB	Monthly	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12	12

Cumulative Impact Sediment Chemistry			A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
Near-field Stations																																																		
	ESC-RNA	4 times per year			12		12				12		12				12		12				12		12				12		12				12		12				12		12				12		12	
	ESC-RNB1	4 times per year			12		12				12		12				12		12				12		12				12		12				12		12				12		12				12		12	
Mid-field Stations																																																		
	ESC-RMA	4 times per year			12		12				12		12				12		12				12		12				12		12				12		12				12		12				12		12	
	ESC-RMB	4 times per year			12		12				12		12				12		12				12		12				12		12				12		12				12		12				12		12	
Capped Pit Stations																																																		
	ESC-RCA1	4 times per year			12		12				12		12				12		12				12		12				12		12				12		12				12		12				12		12	
	ESC-RCB1	4 times per year			12		12				12		12				12		12				12		12				12		12				12		12				12		12				12		12	
Far-Field Stations																																																		
	ESC-RFA	4 times per year			12		12				12		12				12		12				12		12				12		12				12		12				12		12				12		12	
	ESC-RFB	4 times per year			12		12				12		12				12		12				12		12				12		12				12		12				12		12				12		12	
Ma Wan Station																																																		
	MW1	4 times per year			12		12				12		12				12		12				12		12				12		12				12		12				12		12				12		12	

Sediment Toxicity Tests			A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
Near-Pit Stations																																																		
	ESC-TDA	2 times per year					5						5						5						5						5						5						5						5	
	ESC-TDB1	2 times per year					5						5						5						5						5						5						5						5	
Reference Stations																																																		
	ESC-TRA	2 times per year					5						5						5						5						5						5						5						5	
	ESC-TRB	2 times per year					5						5						5						5						5						5						5						5	
Ma Wan Station																																																		
	MW1	2 times per year					5						5						5						5						5						5						5						5	

Tissue/ Whole Body Sampling			A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
Near-Pit Stations																																																		
	ESC-INA	2 times per year					*						*						*						*						*						*						*						*	
	ESC-INB	2 times per year					*						*						*						*						*						*						*						*	
Reference North																																																		
	TNA	2 times per year					*						*						*						*						*						*						*						*	
	TNB	2 times per year					*						*						*						*						*						*						*						*	
Reference South																																																		
	TSA	2 times per year					*						*						*						*						*						*						*						*	
	TSB	2 times per year					*						*						*						*						*						*						*						*	

Demersal Trawling			A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
Near Pit Stations																																																		
	ESC-INA	4 times per year				5	5					5	5					5	5					5	5					5	5					5	5					5	5					5	5	
	ESC-INB	4 times per year				5	5					5	5					5	5					5	5					5	5					5	5					5	5					5	5	
Reference North																																																		
	TNA	4 times per year				5	5					5	5					5	5					5	5					5	5					5	5					5	5					5	5	
	TNB	4 times per year				5	5					5	5					5	5					5	5					5	5					5	5					5	5					5	5	
Reference South																																																		
	TSA	4 times per year				5	5					5	5					5	5					5	5					5	5					5	5					5	5					5	5	
	TSB	4 times per year				5	5					5	5					5	5					5	5					5	5					5	5					5	5					5	5	

Capping			A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
Ebb Tide																																																		
Impact Station Downcurrent																																																		
	ESC-IPE1A	4 times per year																																			3				3		3				3		3	
	ESC-IPE2A	4 times per year																																			3				3		3				3		3	
	ESC-IPE3	4 times per year																																			3				3		3				3		3	
	ESC-IPE4	4 times per year																																			3				3		3				3		3	
	ESC-IPE5	4 times per year																																			3				3		3				3		3	
Intermediate Station Downcurrent																																																		
	ESC-INE1A	4 times per year																																			3				3		3				3		3	
	ESC-INE2A	4 times per year																																			3				3		3				3		3	
	ESC-INE3A	4 times per year																																			3				3		3				3		3	
	ESC-INE4A	4 times per year																																			3				3		3				3		3	
	ESC-INE5A	4 times per year																																			3				3		3				3		3	
Reference Station Upcurrent																																																		
	ESC-RFE1	4 times per year																																			3				3		3				3		3	
	ESC-RFE2	4 times per year																																			3				3		3				3		3	
	ESC-RFE3	4 times per year																																			3				3		3				3		3	
	ESC-RFE4	4 times per year																																			3				3		3				3		3	
	ESC-RFE5	4 times per year																																			3				3		3				3		3	
Ma Wan Station																																																		
	MW1	4 times per year																																			3				3		3				3		3	
Flood Tide																																																		
Impact Station Downcurrent																																																		
	ESC-IPF1	4 times per year																																			3				3		3				3		3	
	ESC-IPF2	4 times per year																																			3				3		3				3		3	
	ESC-IPF3	4 times per year																																			3				3		3				3		3	
Intermediate Station Downcurrent																																																		
	ESC-INF1	4 times per year																																			3				3		3				3		3	
	ESC-INF2	4 times per year																																			3				3		3				3		3	
	ESC-INF3	4 times per year																																			3				3		3				3		3	
Reference Station Upcurrent																																																		
	ESC-RFF1A	4 times per year																																			3				3		3				3		3	
	ESC-RFF2A	4 times per year																																			3				3		3				3		3	
	ESC-RFF3	4 times per year																																			3				3		3				3		3	
Ma Wan Station																																																		
	MW1	4 times per year																																			3				3		3				3		3	

Routine Water Quality Monitoring			A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
Ebb Tide																																																		
Impact Station Downcurrent																																																		
	ESC-IPE1A	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-IPE2A	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-IPE3	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-IPE4	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-IPE5	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
Intermediate Station Downcurrent																																																		
	ESC-INE1A	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-INE2A	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-INE3A	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-INE4A	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-INE5A	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
Reference Station Upcurrent																																																		
	ESC-RFE1	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-RFE2	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-RFE3	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-RFE4	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-RFE5	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
Ma Wan Station																																																		
	MW1	8 times per year	8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
Flood Tide																																																		
Impact Station Downcurrent																																																		
	ESC-IPF1	8 times per year	8	8		8	8		8	8					8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-IPF2	8 times per year	8	8		8	8		8	8					8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-IPF3	8 times per year	8	8		8	8		8	8					8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
Intermediate Station Downcurrent																																																		
	ESC-INF1	8 times per year	8	8		8	8		8	8					8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-INF2	8 times per year	8	8		8	8		8	8					8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-INF3	8 times per year	8	8		8	8		8	8					8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
Reference Station Upcurrent																																																		
	ESC-RFF1A	8 times per year	8	8		8	8		8	8					8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-RFF2A	8 times per year	8	8		8	8		8	8					8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
	ESC-RFF3	8 times per year	8	8		8	8		8	8					8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	
Ma Wan Station																																																		
	MW1	8 times per year	8	8		8	8		8	8					8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8		8	8	

Water Column Profiling			A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
Plume Stations	WCP1	Monthly	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4
	WCP2	Monthly	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4

Benthic Recolonisation Studies			A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
Capped Stations at CMPV																																																		
	ESCV-CPA	2 times per year																																																
	ESCV-CPB	2 times per year																																																
	ESCV-CPC	2 times per year																																																
	ESCV-CPD	2 times per year																																																
Reference Stations																																																		
	RBA	2 times per year																																																
	RBB	2 times per year																																																
	RBC1	2 times per year																																																

Impact Monitoring for Dredging			A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M
Upstream Stations																																																		
	US1	3 times per week				2	2	2																										2	2															
	US2	3 times per week				2	2	2																										2	2															
Downstream Stations																																																		
	DS1	3 times per week				2	2	2																										2	2															
	DS2	3 times per week				2	2	2																										2	2															
	DS3	3 times per week				2	2	2																										2	2															
	DS4	3 times per week				2	2	2																										2	2															
	DS5	3 times per week				2	2	2																										2	2															
Ma Wan Station																																																		
	MW1	3 times per week				2	2	2																										2	2															

Notes:
The number shown in each cell represents the numbers of replicates per monitoring station
Impact Monitoring for Dredging will be scheduled when dredging operations commence.
Benthic Recolonisation Studies for CMP V will be scheduled when capping operation for CMP V is completed.

Annex B

Water Quality Monitoring Results

Table B1 Action and Limit Levels of Water Quality for Dredging, Disposal and Capping Activities at ESC CMP V

Parameter	Action Level	Limit Level
Dissolved Oxygen (DO) (1)	Surface and Mid-depth (2) 5%-ile of baseline data for surface and middle layer = **3.76 mg L^{-1}** and Significantly less than the reference stations mean DO (at the same tide of the same day)	Surface and Mid-depth (2) 1%-ile of baseline data for surface and middle layer = **3.11 mg L^{-1}** (3) and Significantly less than the reference stations mean DO (at the same tide of the same day)
	Bottom 5%-ile of baseline data for bottom layers = **2.96 mg L^{-1}** and Significantly less than the reference stations mean DO (at the same tide of the same day)	Bottom The average of the impact station readings are **<2 mg/L^{-1}** and Significantly less than the reference stations mean DO (at the same tide of the same day)
Depth-averaged Suspended Solids (SS) (4) (5)	95%-ile of baseline data for depth average = **37.88 mg L^{-1}** and 120% of control station's SS at the same tide of the same day	99%-ile of baseline data for depth average = **61.92 mg L^{-1}** and 130% of control station's SS at the same tide of the same day
Depth-averaged Turbidity (Tby) (4) (5)	95%-ile of baseline data = **28.14 NTU** and 120% of control station's Tby at the same tide of the same day	99%-ile of baseline data = **38.32 NTU** and 130% of control station's Tby at the same tide of the same day

Notes:

(1) For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.

(2) The Action and Limit Levels for DO for Surface & Middle layers were calculated from the combined pool of baseline surface layer data and baseline middle layer data.

(3) Given the Action Level for DO for Surface & Middle layers has already been lower than 4 mg L^{-1}, it is proposed to set the Limit Level at 3.11 mg L^{-1} which is the first percentile of the baseline data.

(4) "Depth-averaged" is calculated by taking the arithmetic means of reading of all three depths.

(5) For turbidity and SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.

Table B2 Water Column Profiling Results for ESC CMP Vb in July 2020

Stations	Temp (°C)	Salinity (ppt)	Turbidity (NTU)	Dissolved Oxygen (%)	Dissolved Oxygen (mg L^{-1})	pH	Suspended Solids (mg L^{-1})
WCP 1 (Downstream)	28.76	17.21	5.07	90.43	6.35	7.91	5.73
WCP 2 (Upstream)	28.20	19.08	9.71	82.83	5.81	7.90	8.95
WQO (Wet Season)	N/A	17.17-20.98#	N/A	N/A	>4	6.5-8.5	10.8

Note:
#Not exceeding 10% of natural ambient level which is the result obtained from the Reference Station.
Cell shaded yellow / red indicate value exceeding the Action/Limit levels.
Cell shaded grey indicate value exceeding the WQO.

Table B3 In-situ Monitoring Results for Routine Water Quality Monitoring of ESC CMPs in July 2020

Sampling Period	Stations	Temp (°C)	Salinity (ppt)	Turbidity (NTU)	Dissolved Oxygen (%)	Dissolved Oxygen (mg L^{-1})	pH (mg L^{-1})
July 2020	RFE (Reference)	28.19	19.08	4.73	85.80	6.02	7.90
	IPE (Impact)	27.88	20.16	4.66	82.18	5.76	7.87
	INE (Intermediate)	28.12	19.13	3.96	82.60	5.80	7.88
	Ma Wan	26.28	25.82	2.67	72.05	5.03	7.69
	WQO	N/A	17.18- 20.99#	N/A	N/A	>4	6.5-8.5

Notes:
#Not exceeding 10% of natural ambient level which is the result obtained from the Reference Station.
Cell shaded yellow / red indicate value exceeding the Action/Limit levels.
Cell shaded grey indicate value higher than the WQO.

Table B4 Laboratory Results for Routine Water Quality Monitoring of ESC CMPs in July 2020

Sampling Period	Stations	As (µg/L)	Cd (µg/L)	Cr (µg/L)	Cu (µg/L)	Pb (µg/L)	Hg (µg/L)	Ni (µg/L)	Ag (µg/L)	Zn (µg/L)	NH_3 (mg/L)	TIN (mg/L)	BOD_5 (mg/L)	SS (mg/L)
July 2020	RFE	2.22	<LOR	1.29	11.03	0.93	<LOR	<LOR	<LOR	14.00	0.10	0.93	2.25	7.40
	IPE	2.14	<LOR	1.31	32.01	0.80	<LOR	0.53	<LOR	10.78	0.12	0.93	2.09	7.33
	INE	2.21	<LOR	1.30	33.43	0.93	<LOR	<LOR	<LOR	11.80	0.11	0.99	2.05	6.20
	Ma Wan	2.19	<LOR	1.59	10.53	1.76	<LOR	0.63	<LOR	46.61	0.16	0.78	2.73	5.94

WQO of TIN: 0.5 mg/L
Wet Season WQO of SS : 10.8 mg/L

Notes:
<LOR indicates the concentrations of metals and metalloids are below the limit of reporting
Cell shaded yellow / red indicate value exceeding the Action/Limit levels.
Cell shaded grey indicate value higher than the WQO.

Annex C

Graphical Presentations

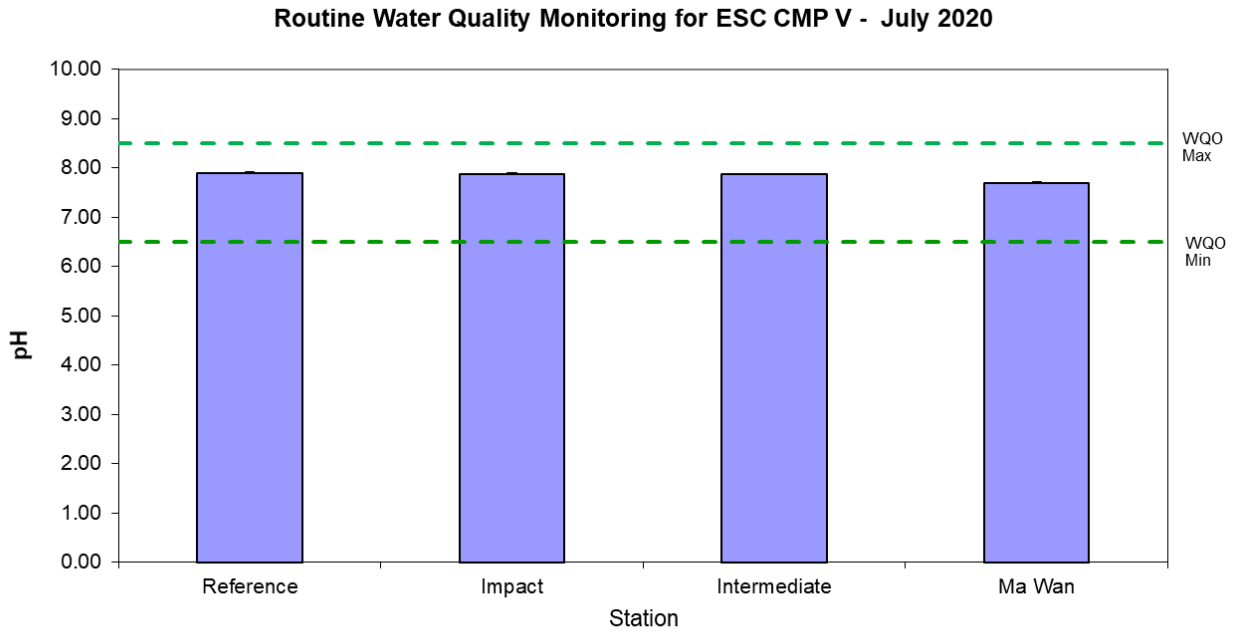

Figure 1: Level of pH recorded during Routine Water Quality Monitoring for disposal operations at ESC CMP V in July 2020.

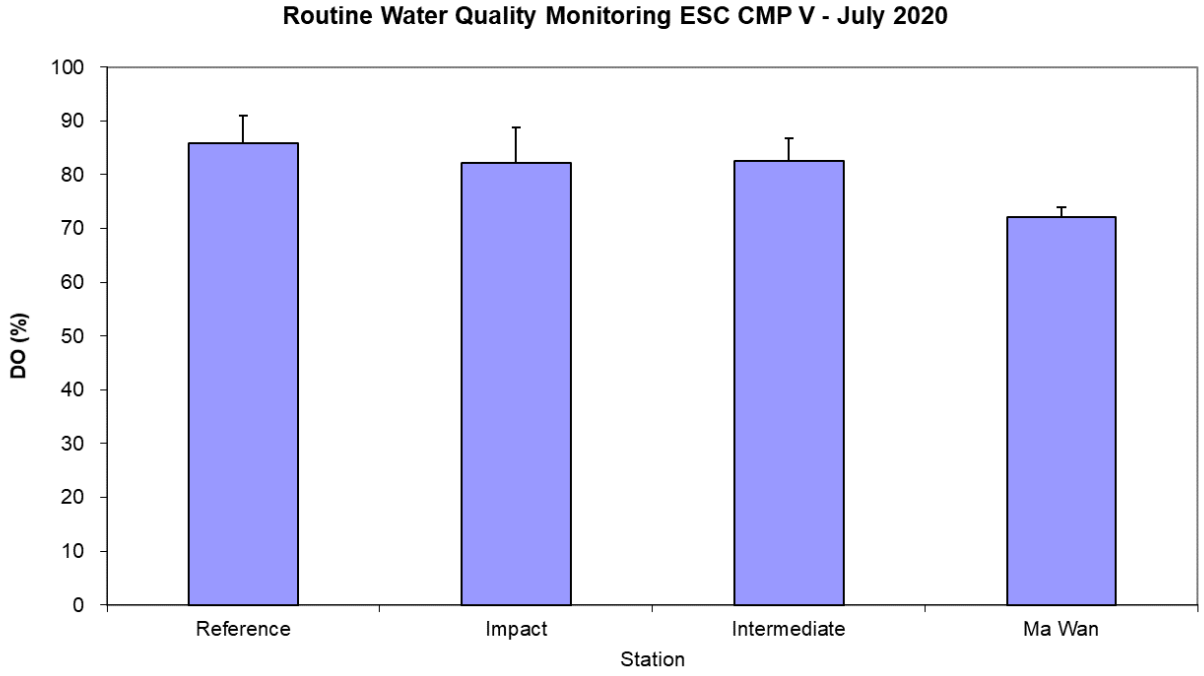

Figure 2: Level of Dissolved Oxygen (DO) (% saturation; mean + SD) recorded during Routine Water Quality Monitoring for disposal operations at ESC CMP V in July 2020.

Source: P:\Projects\0400720 CEDD CMP EM&A 2017-2020\02 Deliverable\05 CMP Monthly Report\40 Monthly July 2020

Date: August 2020

Environmental Resources Management

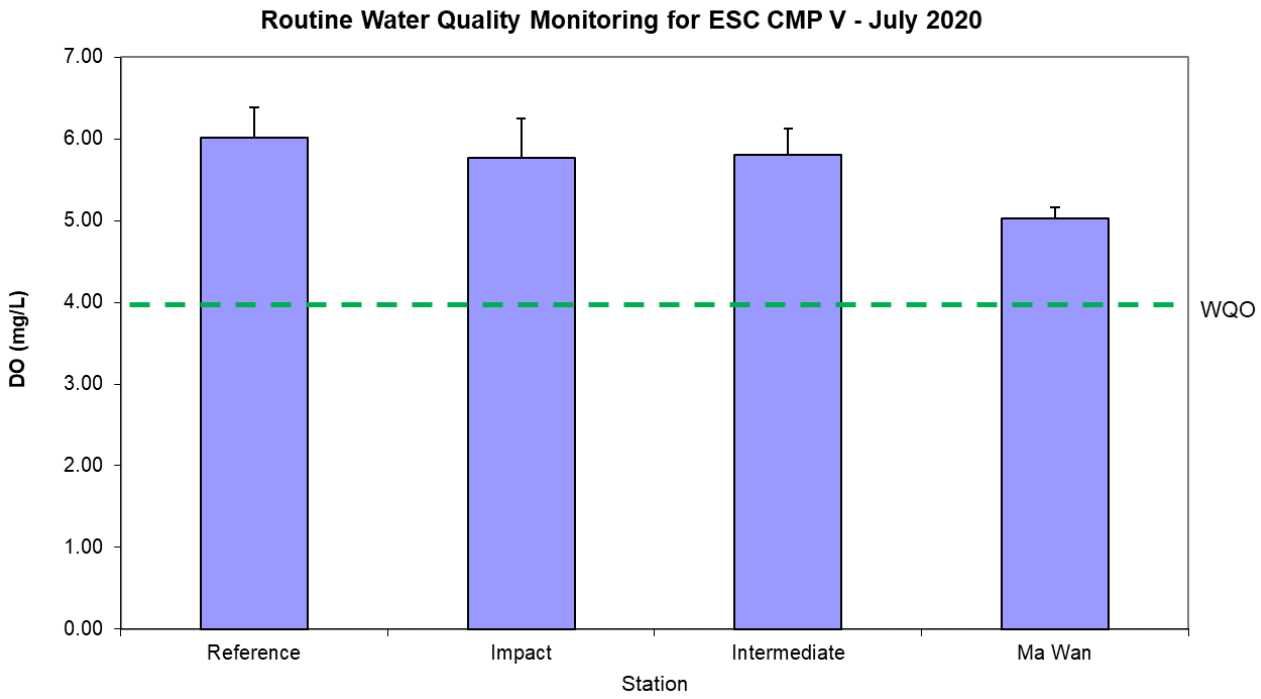

Figure 3: Concentration of Dissolved Oxygen (DO) (mg/L; mean + SD) recorded during Routine Water Quality Monitoring for disposal operations at ESC CMP V in July 2020.

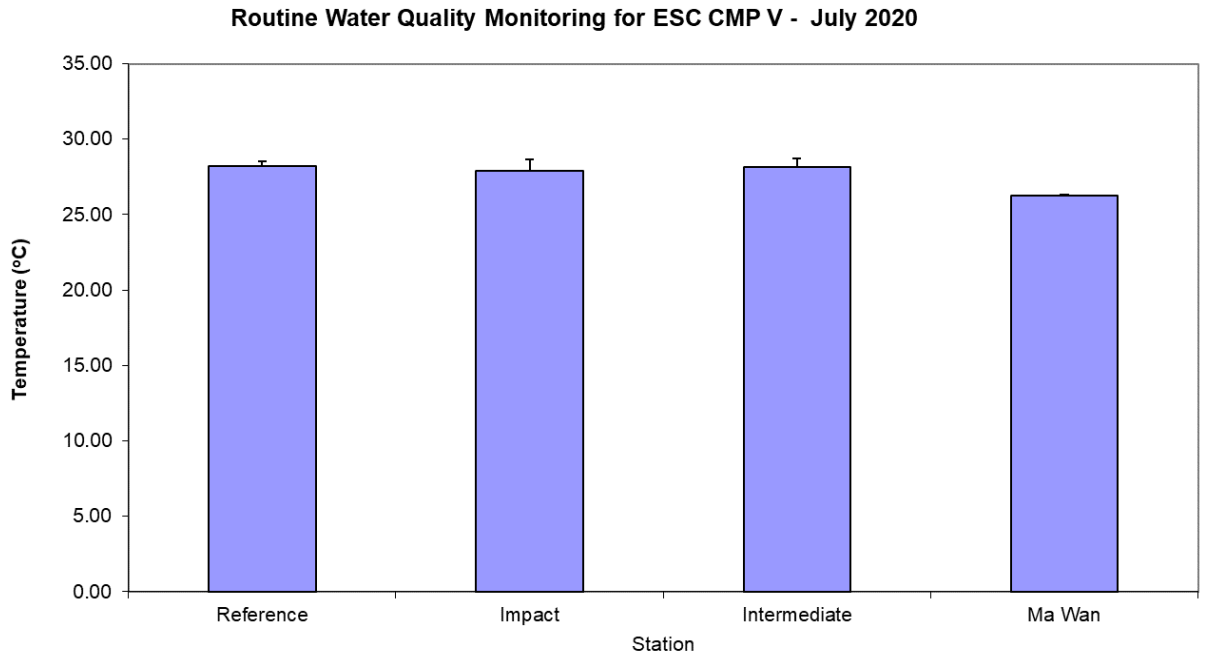

Figure 4: Level of Temperature (˚C; mean + SD) recorded during Routine Water Quality Monitoring for disposal operations at ESC CMP V in July 2020.

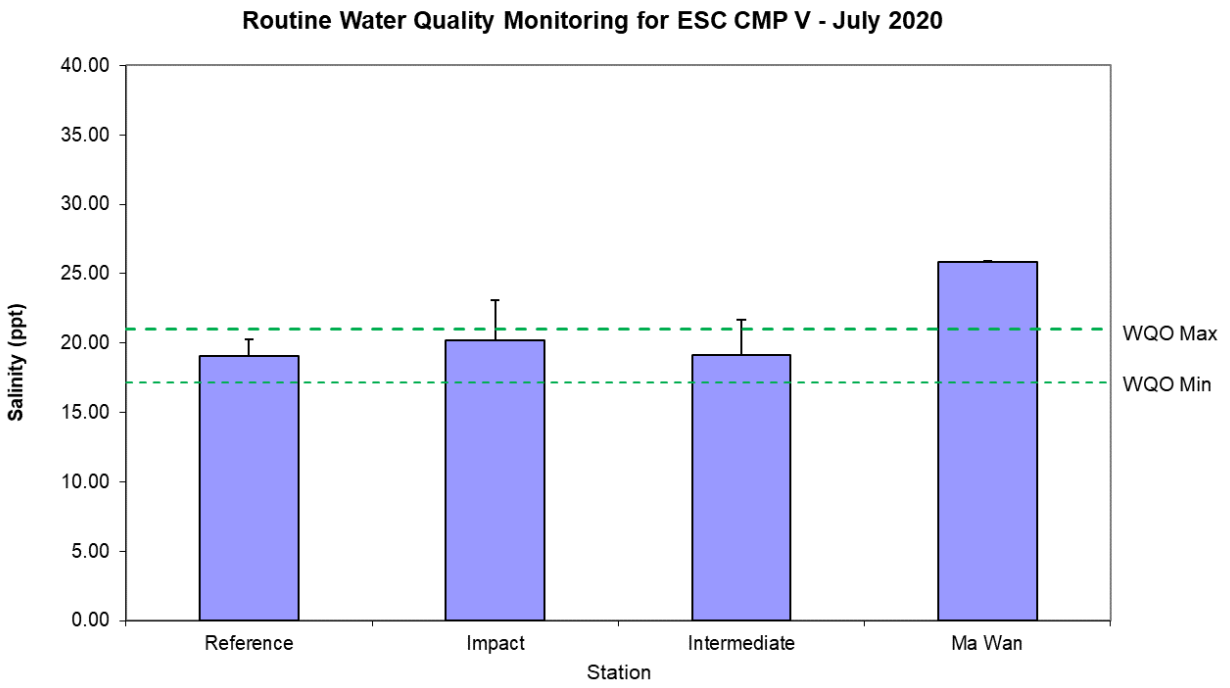

Figure 5: Level of Salinity (ppt; mean + SD) recorded during Routine Water Quality Monitoring for disposal operations at ESC CMP V in July 2020.

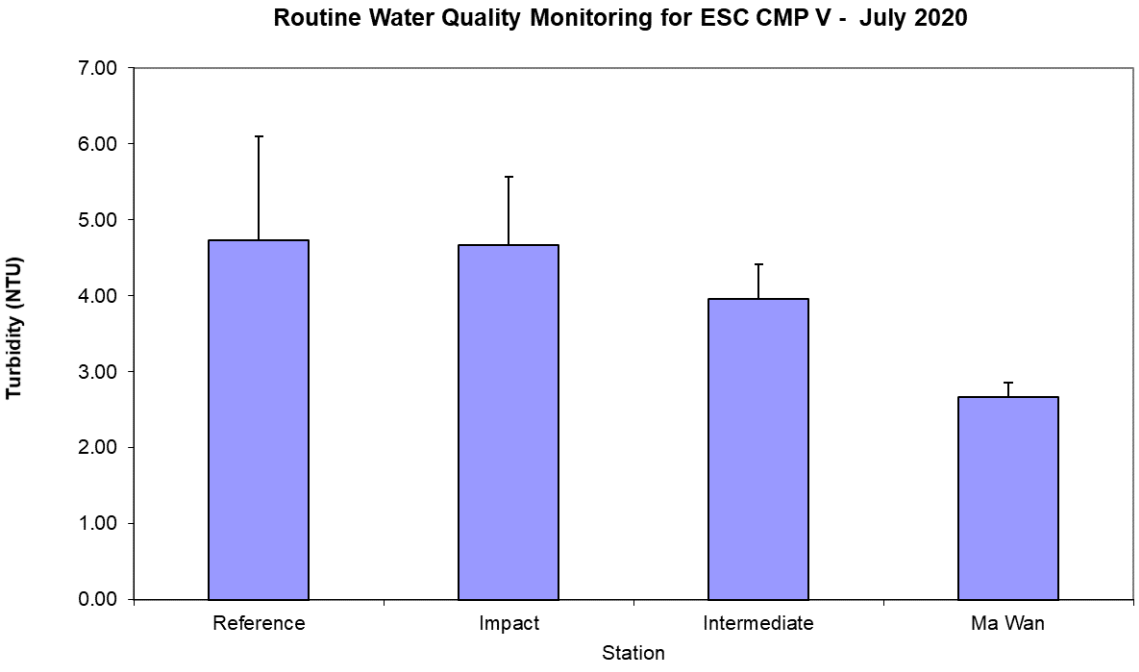

Figure 6: Levels of Turbidity (NTU; mean + SD) recorded during Routine Water Quality Monitoring for disposal operations at ESC CMP V in July 2020.

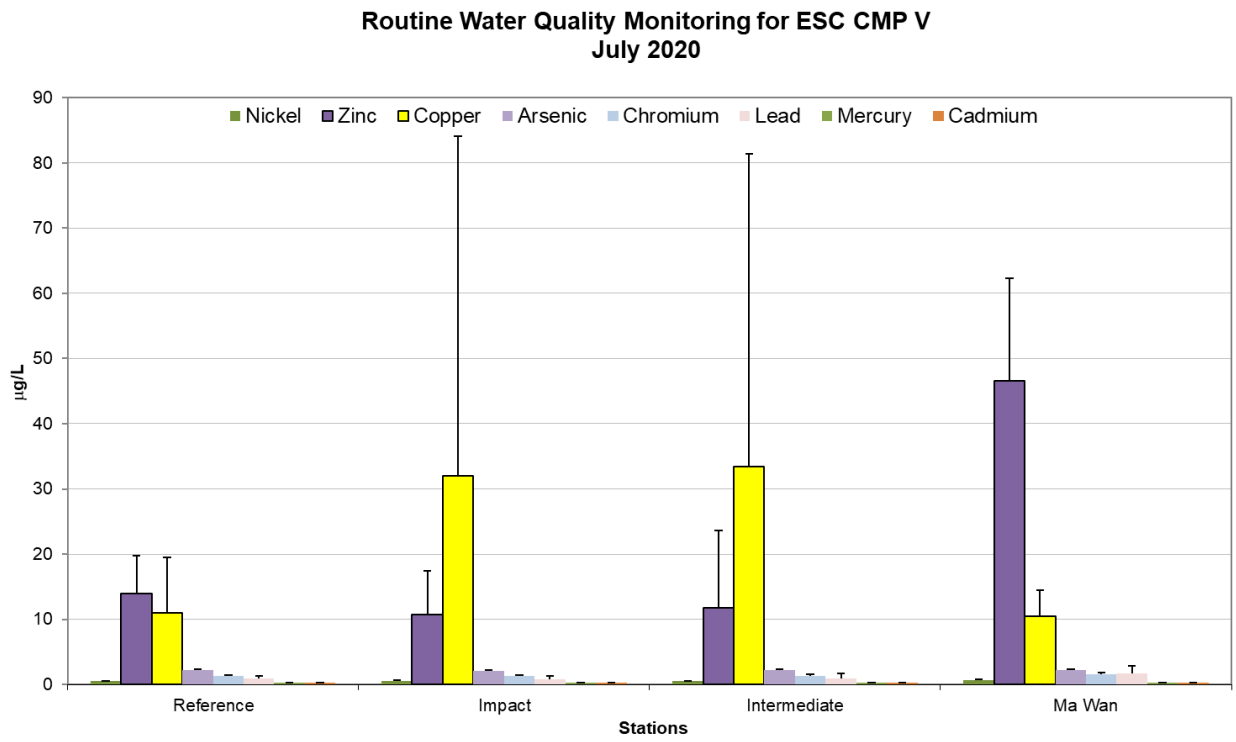

Figure 7: Concentration of Arsenic, Cadmium, Chromium, Copper, Lead, Mercury, Nickel and Zinc (µg/L; mean + SD) in water samples collected from Routine Water Quality Monitoring for disposal operations at ESC CMP V in July 2020.

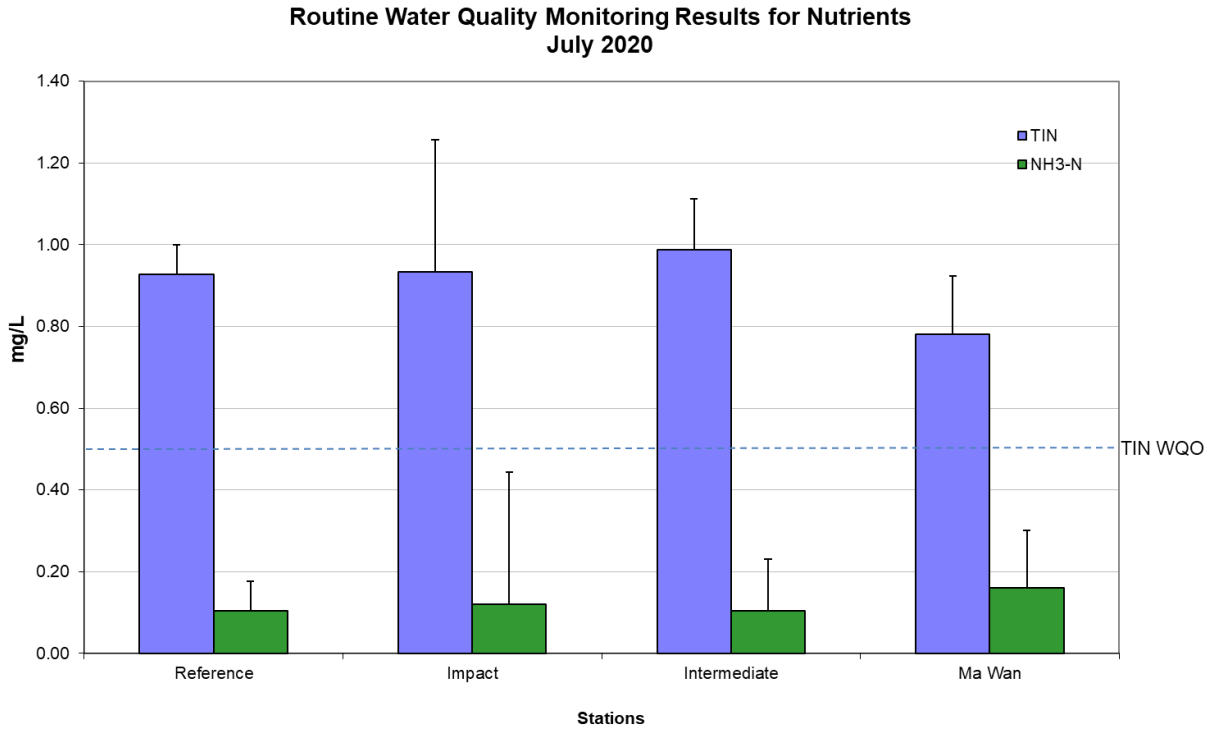

Figure 8: Concentration of Total Inorganic Nitrogen (TIN) and Ammonia Nitrogen (NH3-N) (mg/L; mean + SD) in water samples collected from Routine Water Quality Monitoring for disposal operations at ESC CMP V in July 2020.

Source: P:\Projects\0400720 CEDD CMP EM&A 2017-2020\02 Deliverable\05 CMP Monthly Report\40 Monthly July 2020

Date: August 2020

Environmental Resources Management

ERM

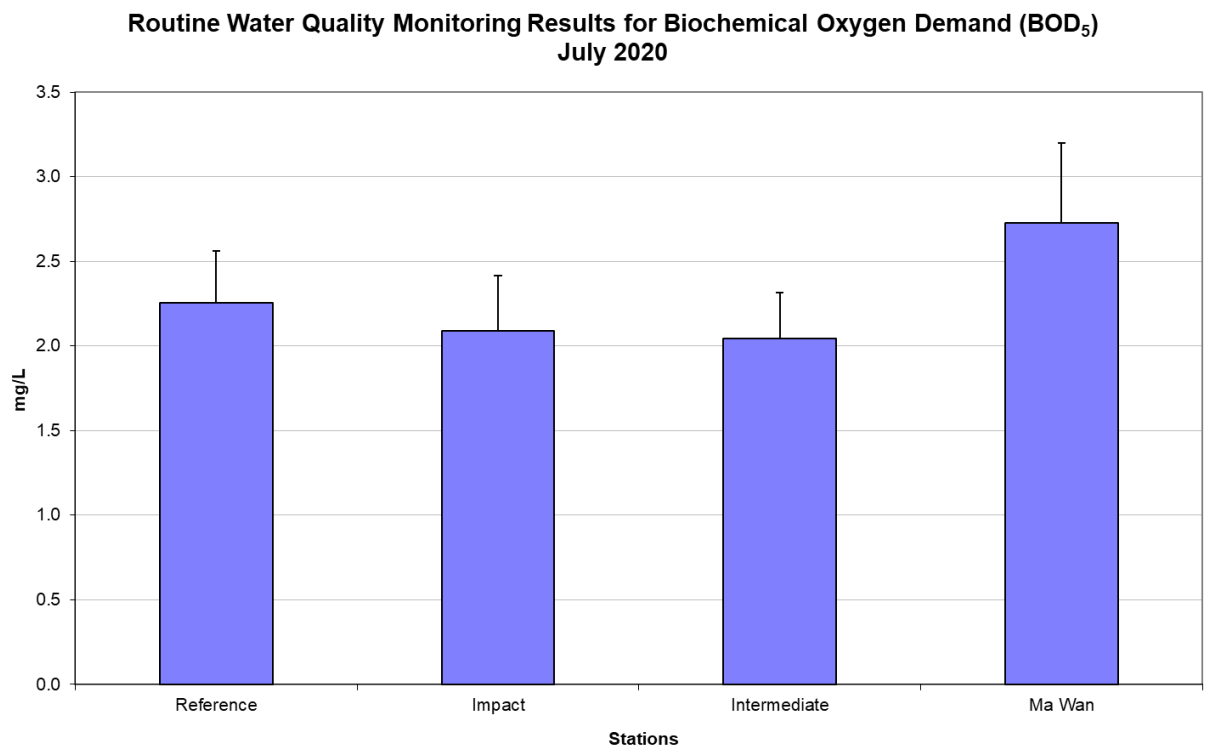

Figure 9: Level of Biochemical Oxygen Demand (BOD_5) (mg/L; mean + SD) in water samples collected from Routine Water Quality Monitoring for disposal operations at ESC CMP V in July 2020.

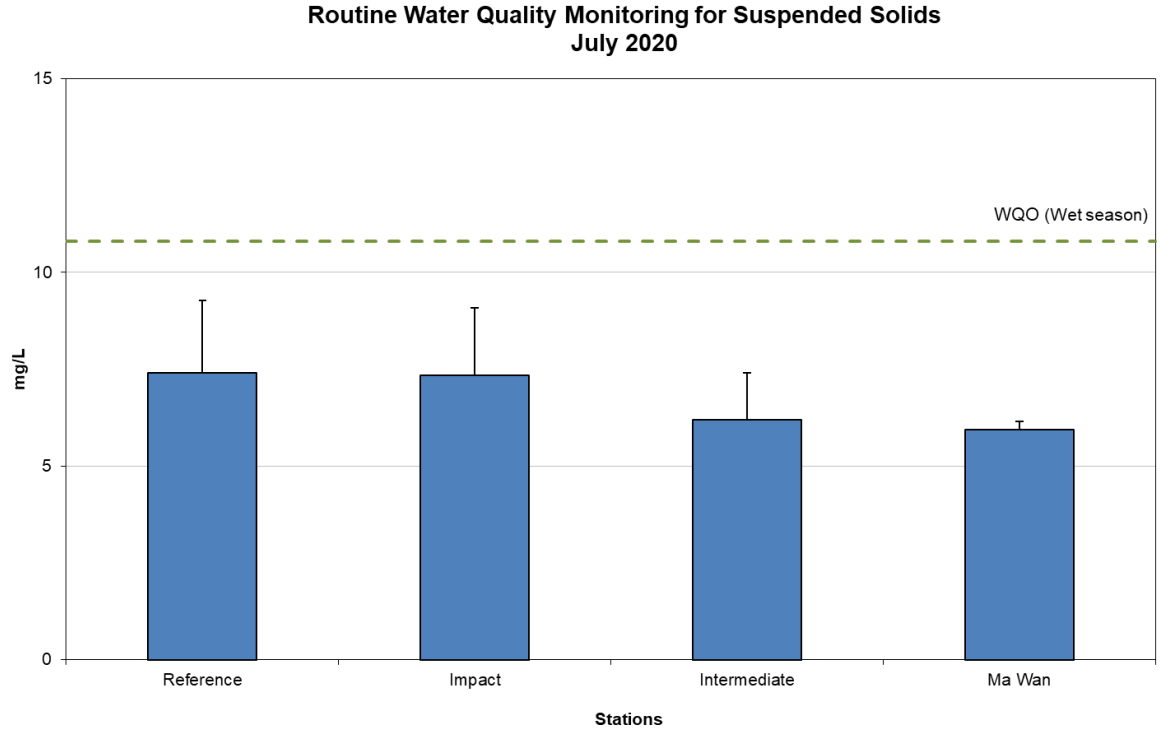

Figure 10: Concentration of Suspended Solids (SS) (mg/L; mean + SD) in water samples collected from Routine Water Quality Monitoring for disposal operations at ESC CMP V in July 2020.

Source: P:\Projects\0400720 CEDD CMP EM&A 2017-2020\02 Deliverable\05 CMP Monthly Report\40 Monthly July 2020

Date: August 2020

Environmental Resources Management

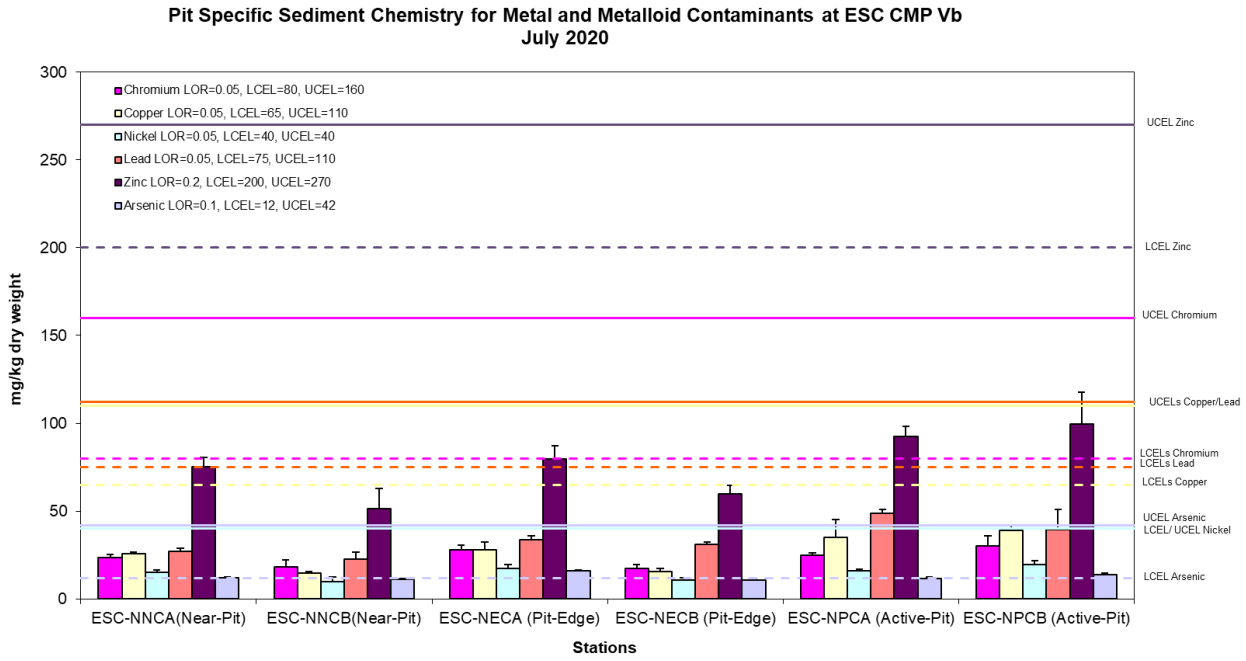

Figure 11: Concentration of Metals and Metalloid (Cr, Cu, Ni, Pb, Zn, As; mg/kg dry weight; mean +SD) in sediment samples collected from Pit Specific Sediment Chemistry Monitoring for ESC CMP Vb in July 2020.

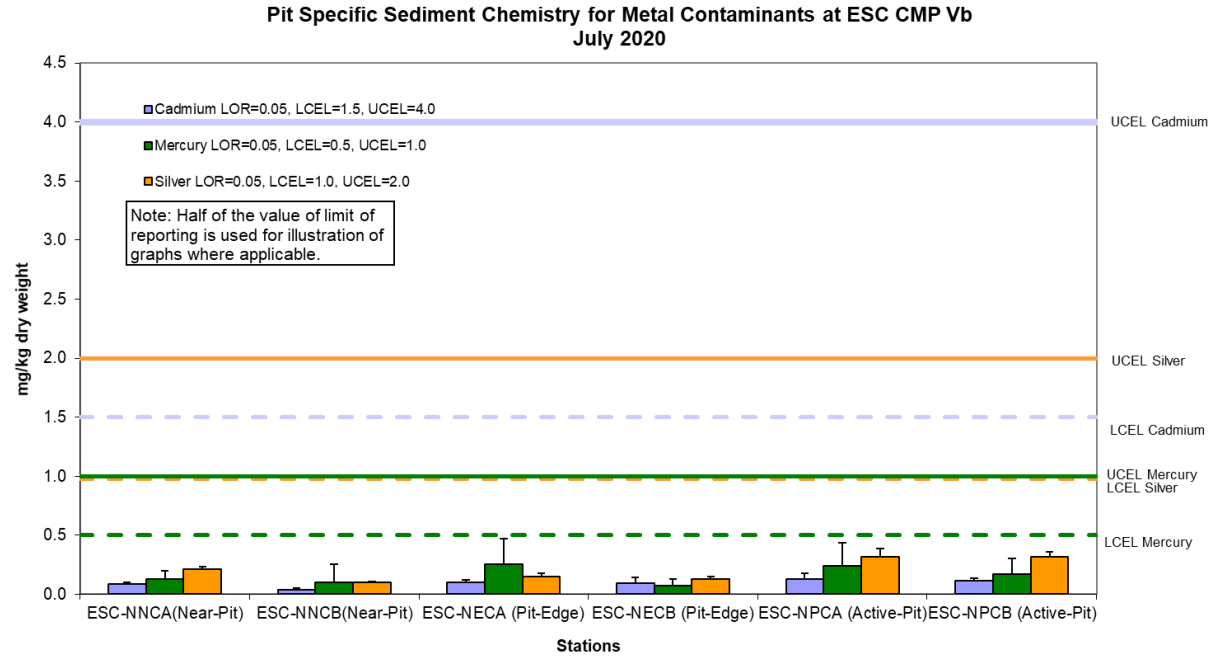

Figure 12: Concentration of Metals (Cd, Hg, Ag; mg/kg dry weight; mean +SD) in sediment samples collected from Pit Specific Sediment Chemistry Monitoring for ESC CMP Vb in July 2020.

Source: P:\Projects\0400720 CEDD CMP EM&A 2017-2020\02 Deliverable\05 CMP Monthly Report\40 Monthly July 2020

Date: August 2020

Environmental Resources Management

ERM

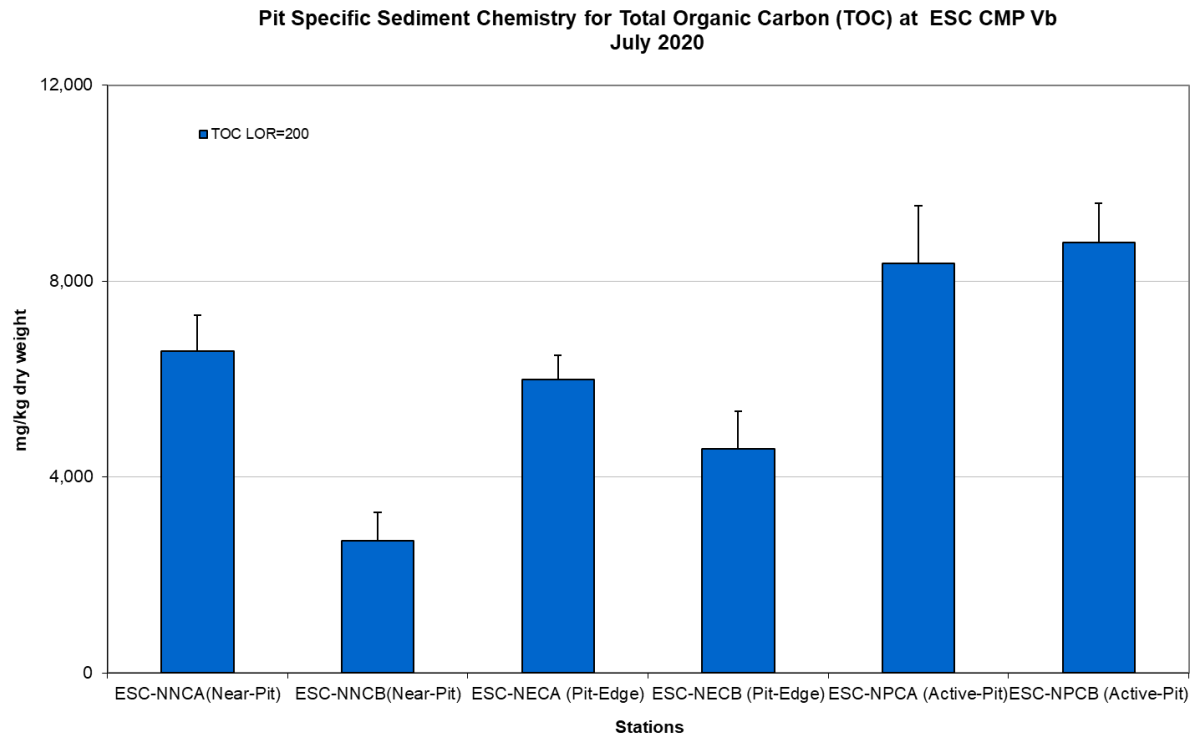

Figure 13: Concentration of Total Organic Carbon (TOC) (mg/kg dry weight; mean +SD) in sediment samples collected from Pit Specific Sediment Chemistry Monitoring for ESC CMP Vb in July 2020.

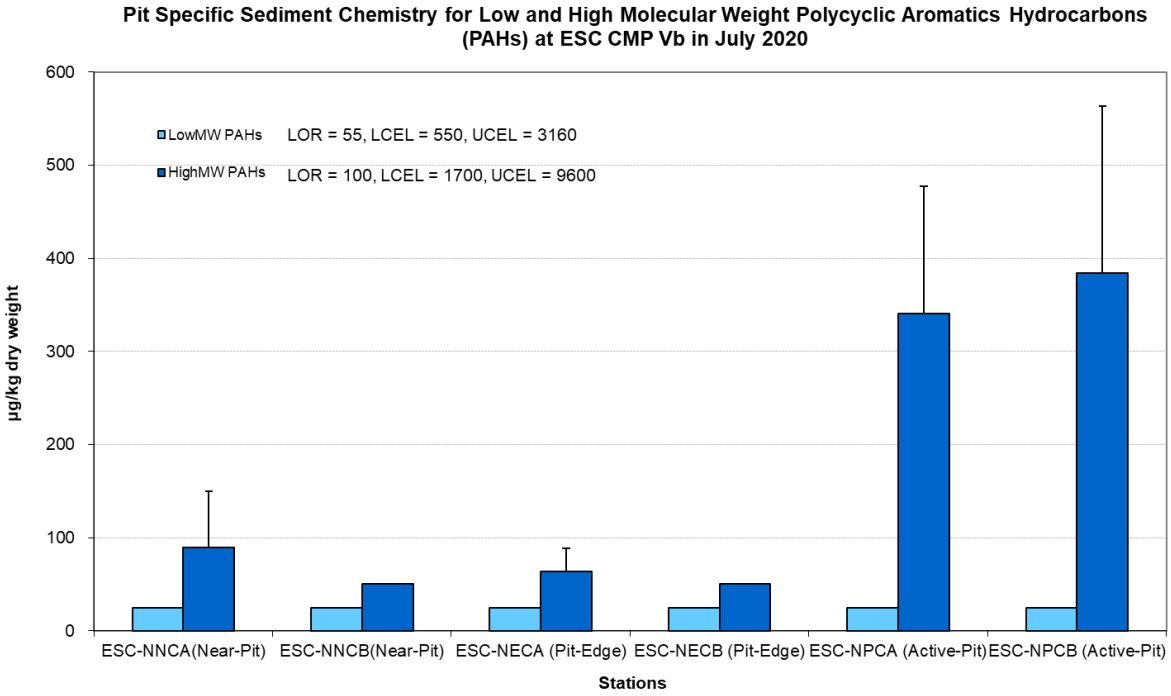

Figure 14: Concentration of Low and High Molecular Weight Polycyclic Aromatics (mg/kg dry weight; mean +SD) in sediment samples collected from Pit Specific Sediment Chemistry Monitoring for ESC CMP Vb in July 2020.

Source: P:\Projects\0400720 CEDD CMP EM&A 2017-2020\02 Deliverable\05 CMP Monthly Report\40 Monthly July 2020

Date: August 2020

Environmental Resources Management

ERM

Annex D

Study Programme

Task Name	Start	Finish
Commencement of Agreement No. CE 63/2016 (EP)	Sat 1/4/17	Sat 1/4/17
Project Management and General Deliverables	**Mon 3/4/17**	**Mon 5/4/21**
For the disposal facilities to the East of Sha Chau (ESC) (between 2017 and 2021) and the South of The Brothers (SB) (between 2017 and 2018)	**Sat 1/4/17**	**Fri 1/10/21**
Draft Report on Review of EM&A Manual	Tue 2/5/17	Tue 2/5/17
Final Report on Review of EM&A Manual	Tue 23/5/17	Tue 23/5/17
Regular Review of EM&A Manual	**Wed 2/5/18**	**Sat 2/5/20**
Regular Site Inspections of CMP Contractors	Sat 1/4/17	Wed 31/3/21
Participate in Liaison Group Meetings/ Consultations as required by CEDD	Sat 1/4/17	Wed 31/3/21
Submission of Monthly EM&A Report	**Sun 14/5/17**	**Sun 14/3/21**
Submission of Quarterly EM&A Report	**Fri 14/7/17**	**Wed 14/4/21**
Submission of Annual EM&A Report	**Sun 14/1/18**	**Thu 14/1/21**
Submission of Annual Risk Assessment Report	**Thu 14/6/18**	**Mon 14/6/21**
Submission of Draft Final Report (including database of all data collected)	Fri 23/7/21	Fri 23/7/21
Submission of Final Report (including database of all data collected)	Fri 27/8/21	Fri 27/8/21
Submission of Draft Executive Summary	Fri 27/8/21	Fri 27/8/21
Submission of Final Executive Summary	Fri 1/10/21	Fri 1/10/21
For East Tung Lung Chau Disposal Facility (subject to the actual disposal programme to be confirmed by CEDD)	**Sun 14/10/18**	**Fri 14/12/18**
Submission of Monthly EM&A Report	**Sun 14/10/18**	**Fri 14/12/18**
Submission of Quarterly EM&A Report	Fri 14/12/18	Fri 14/12/18
Submission of Annual EM&A Report	Fri 14/12/18	Fri 14/12/18

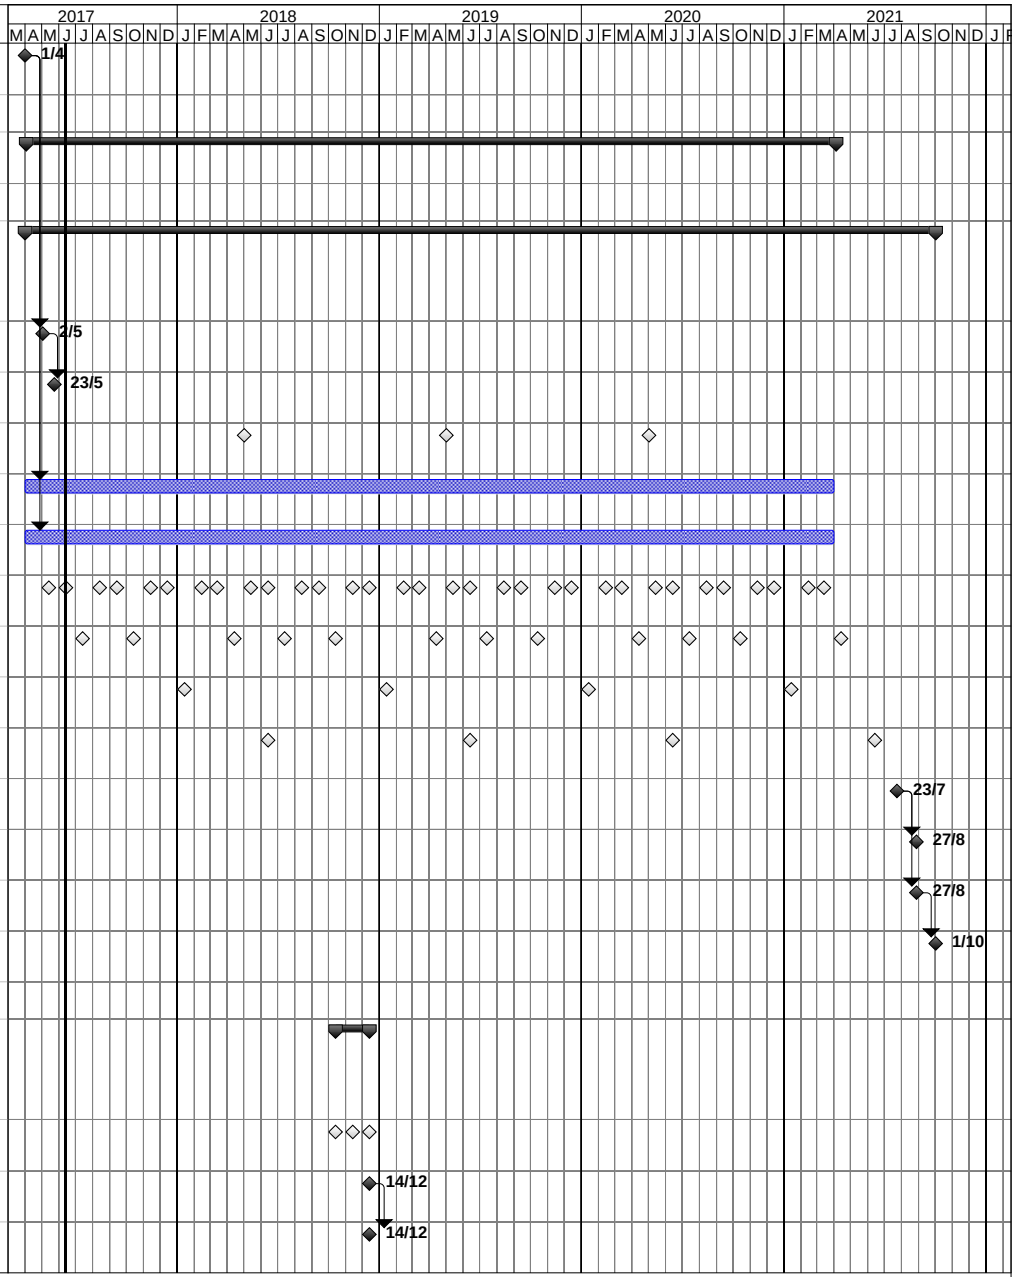

Study Programme
Tue 13/6/17

Task | Milestone | Summary | Rolled Up Milestone
